
DFW Airfield Storyboards - DRAFT

January 6, 2023



Runway Approach and Departure Impact

Runway Name		FY2023										FY2024										FY2025				FY2026								
		J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A									S				
Thresholds	RWY 13R																																	
	RWY 31L																																	
	RWY 18R																																	
	RWY 36L																																	
	RWY 18L	Airfield Remediation																																
	RWY 36R																																	
	RWY 17R									Runway Rehabilitation (17R/35L Full Closure)										17R MALSR OTS														
	RWY 35L					35L MALSR OTS (Departures Only)														35L MALSR OTS														
	RWY 17C																																	
	RWY 35C																																	
	RWY 17L																																	
	RWY 35R																																	
	RWY 13L																																	
	RWY 31R																																	


Key

Day Work

Night Work



For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

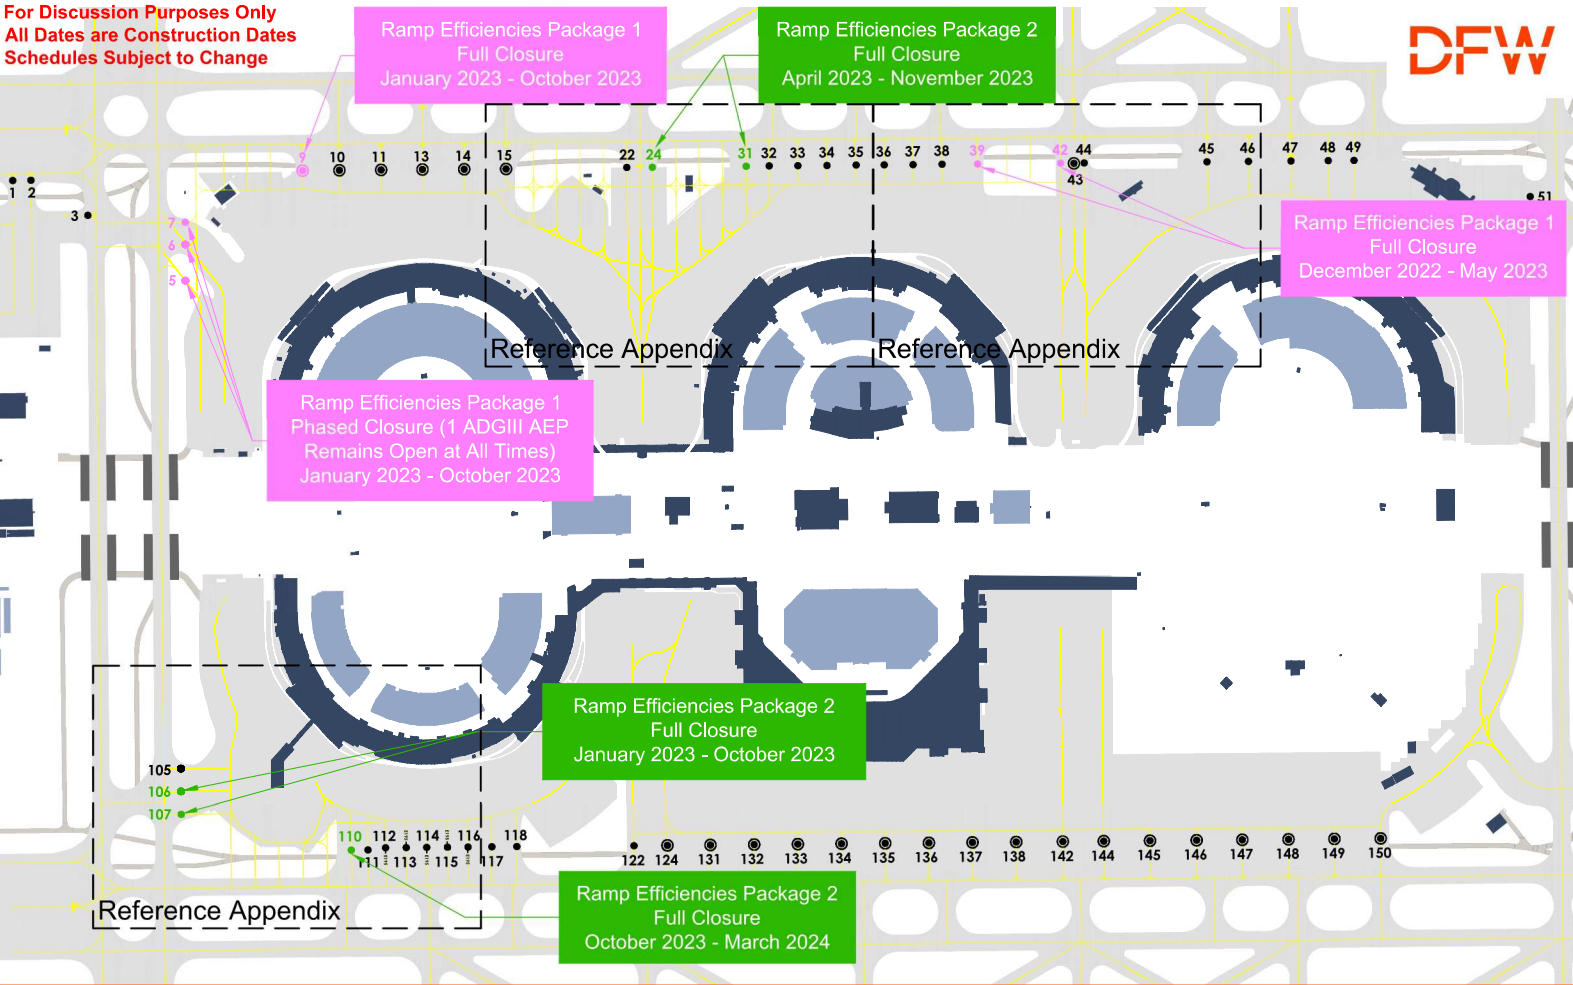


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts


North Flow: TBD by FAA

South Flow: TBD by FAA

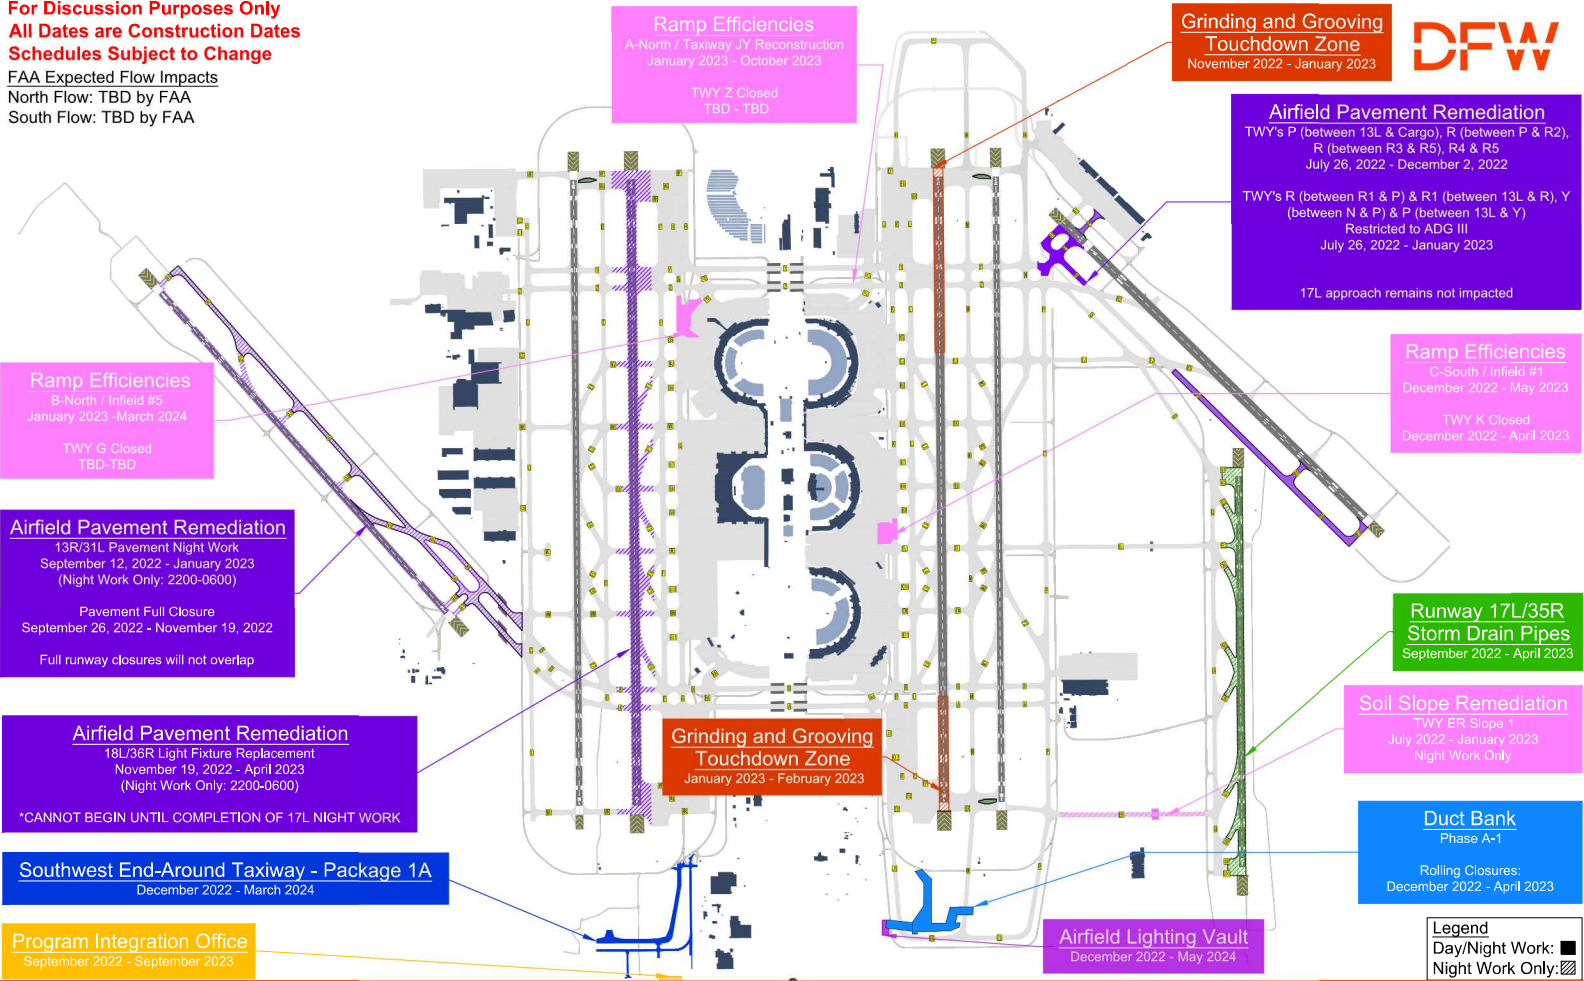

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change


FAA Expected Flow Impacts
 North Flow: TBD by FAA
 South Flow: TBD by FAA

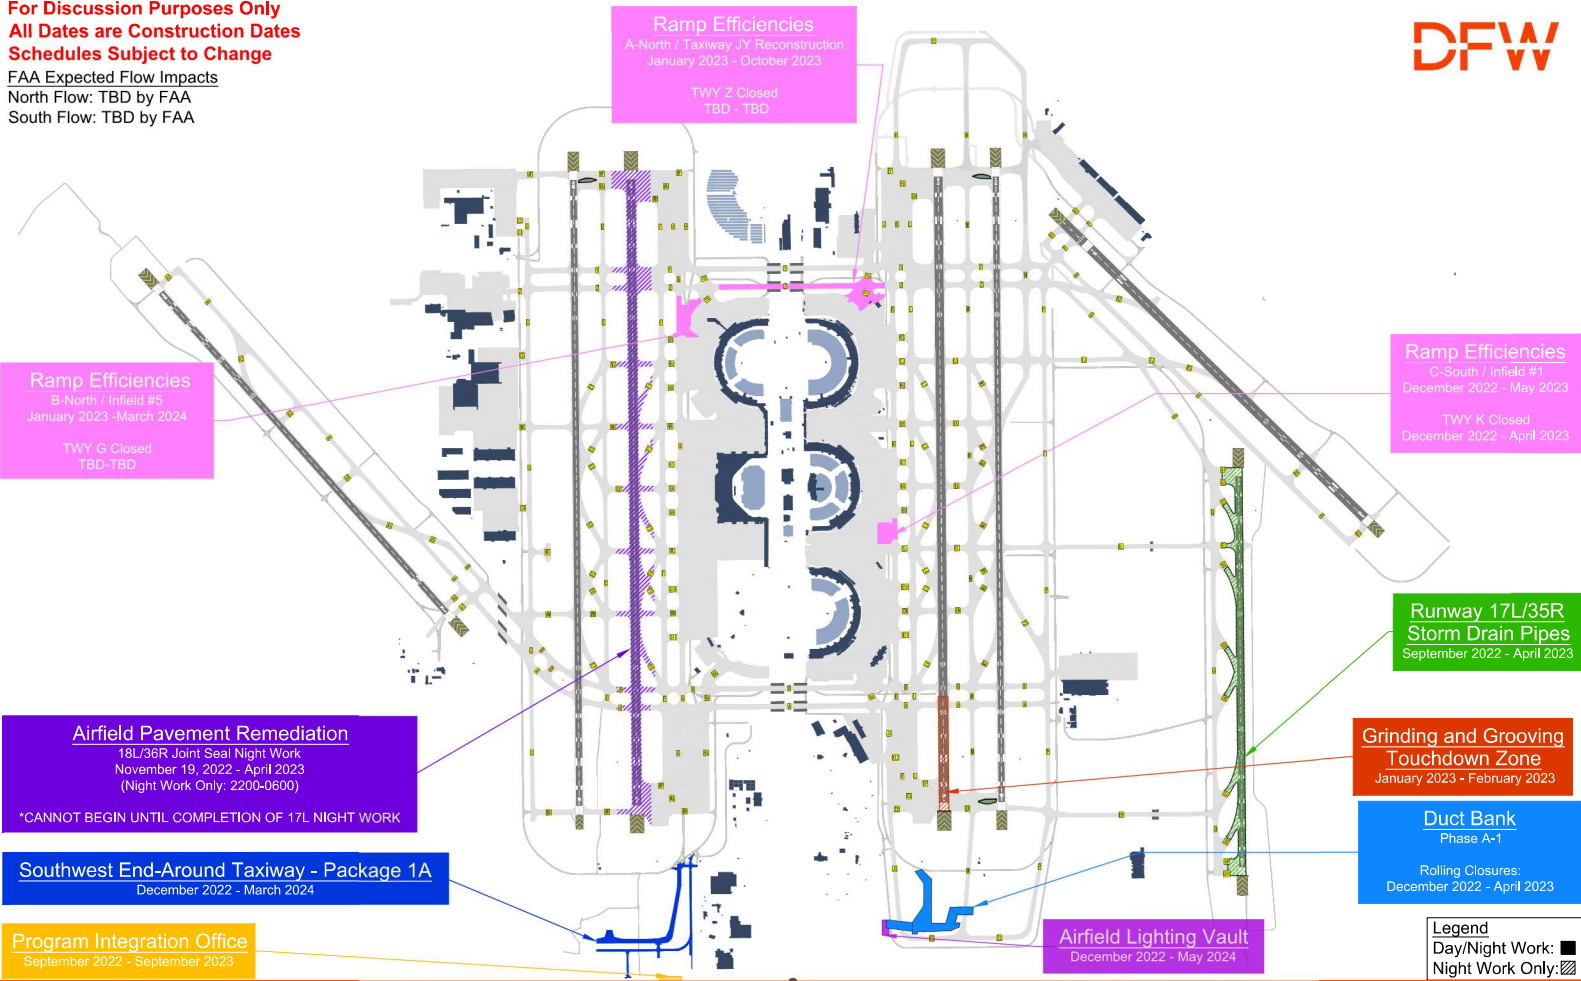

Legend
 Day/Night Work: ■
 Night Work Only: ▨

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
 North Flow: TBD by FAA
 South Flow: TBD by FAA

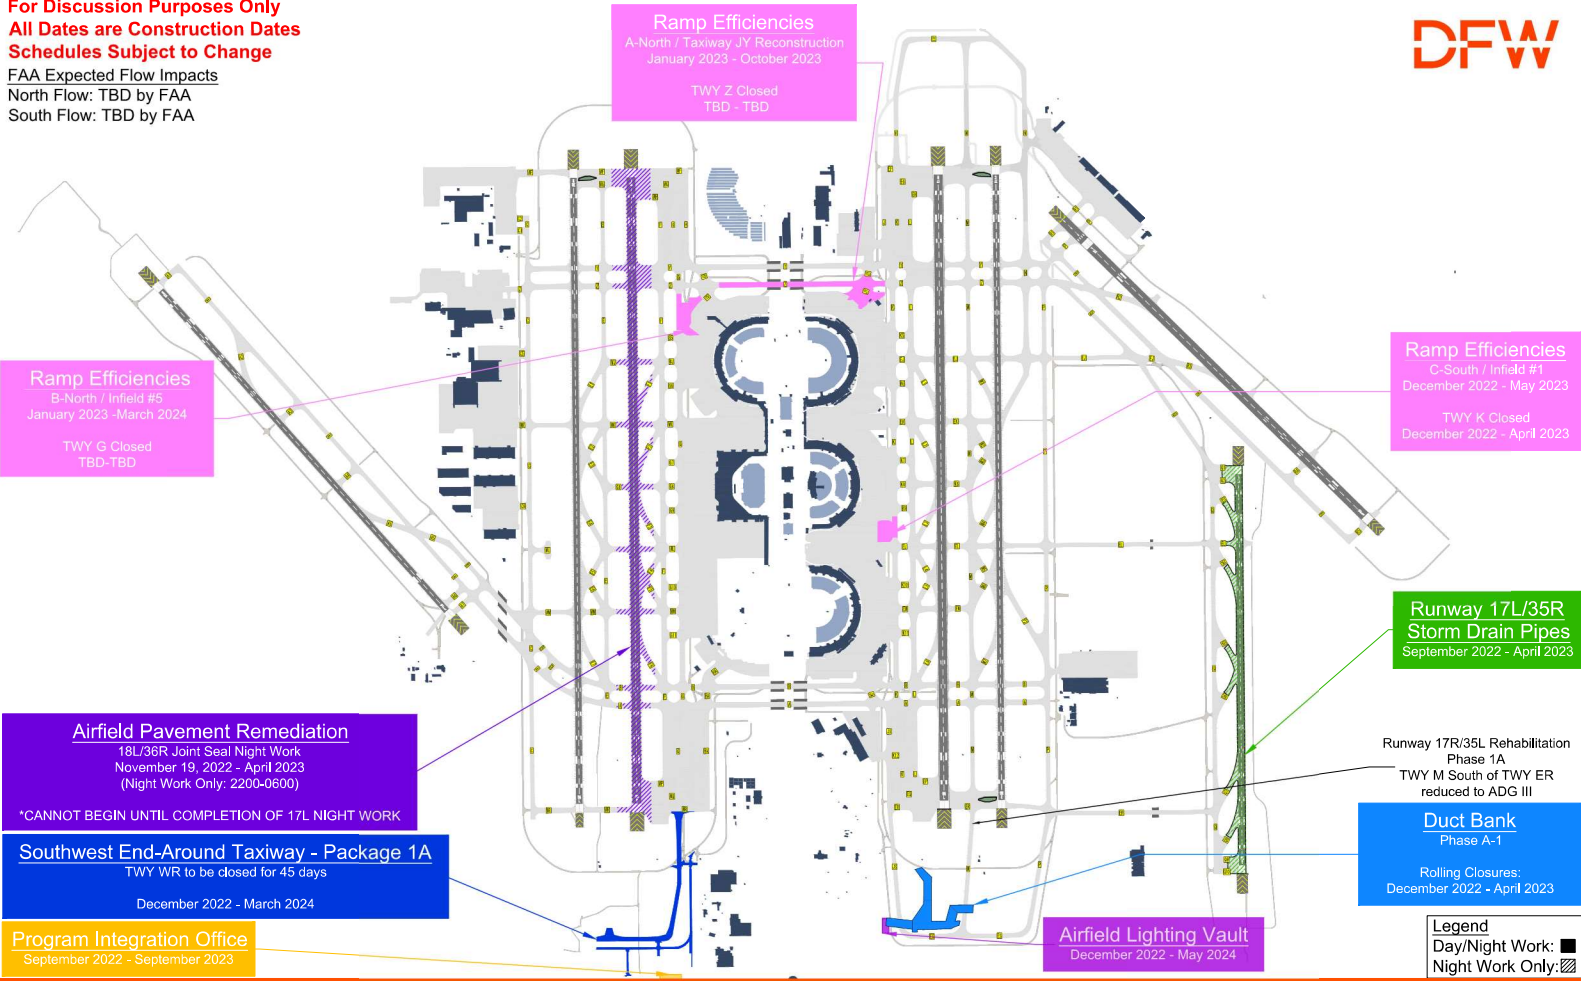


Legend
 Day/Night Work: ■
 Night Work Only: ▨

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts


North Flow: TBD by FAA

South Flow: TBD by FAA

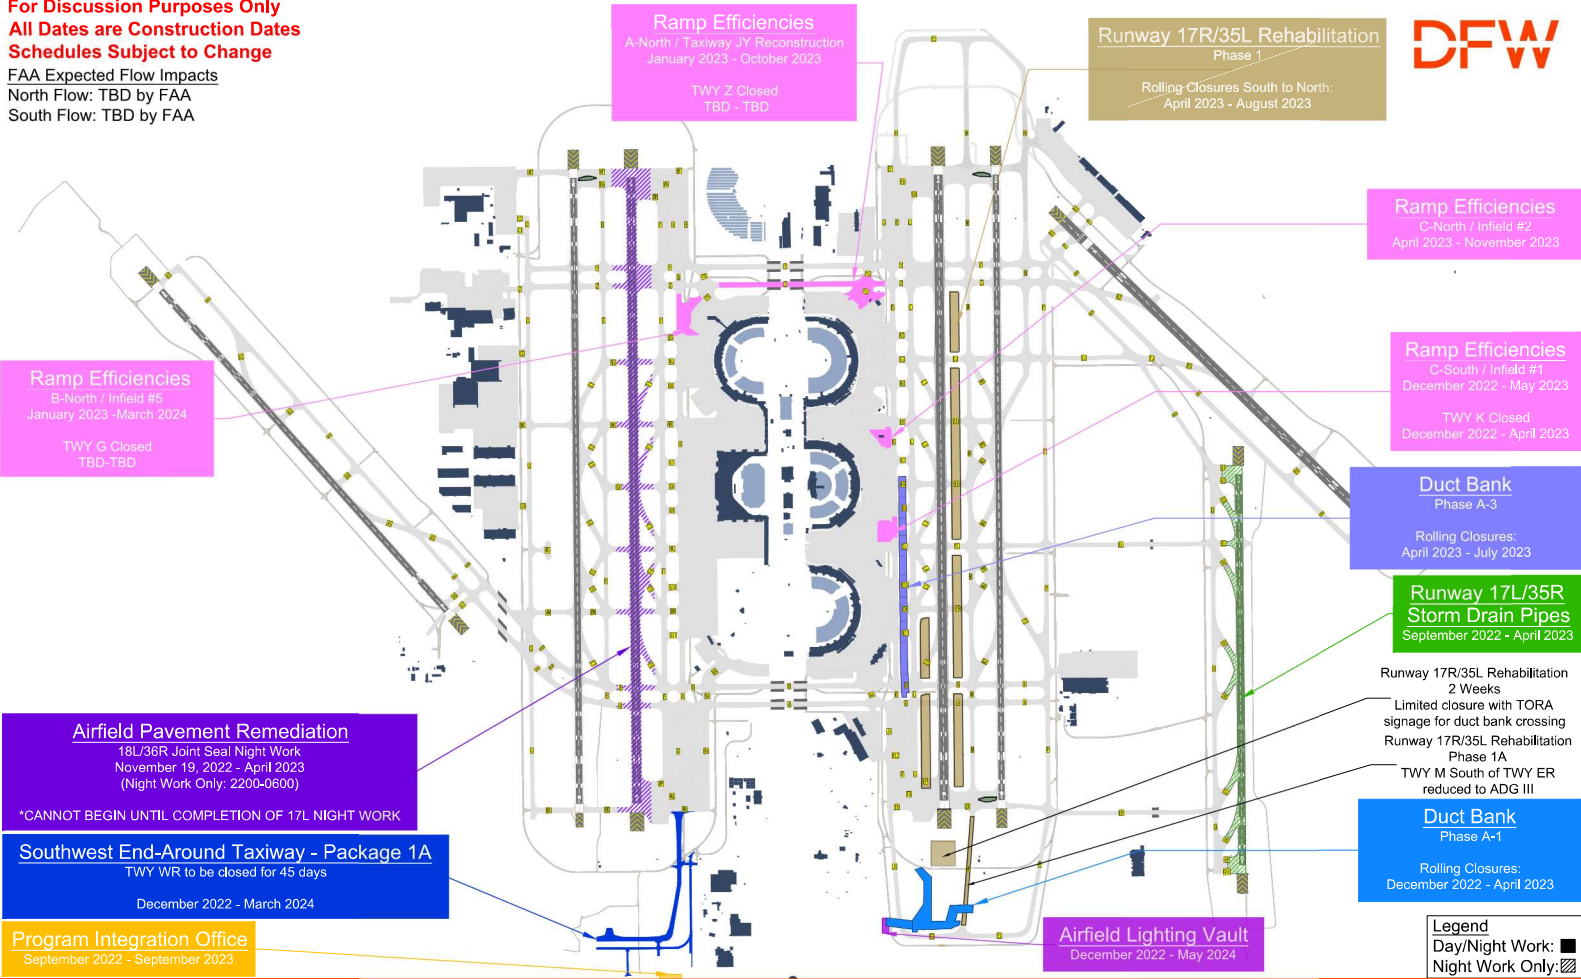

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
 North Flow: TBD by FAA
 South Flow: TBD by FAA

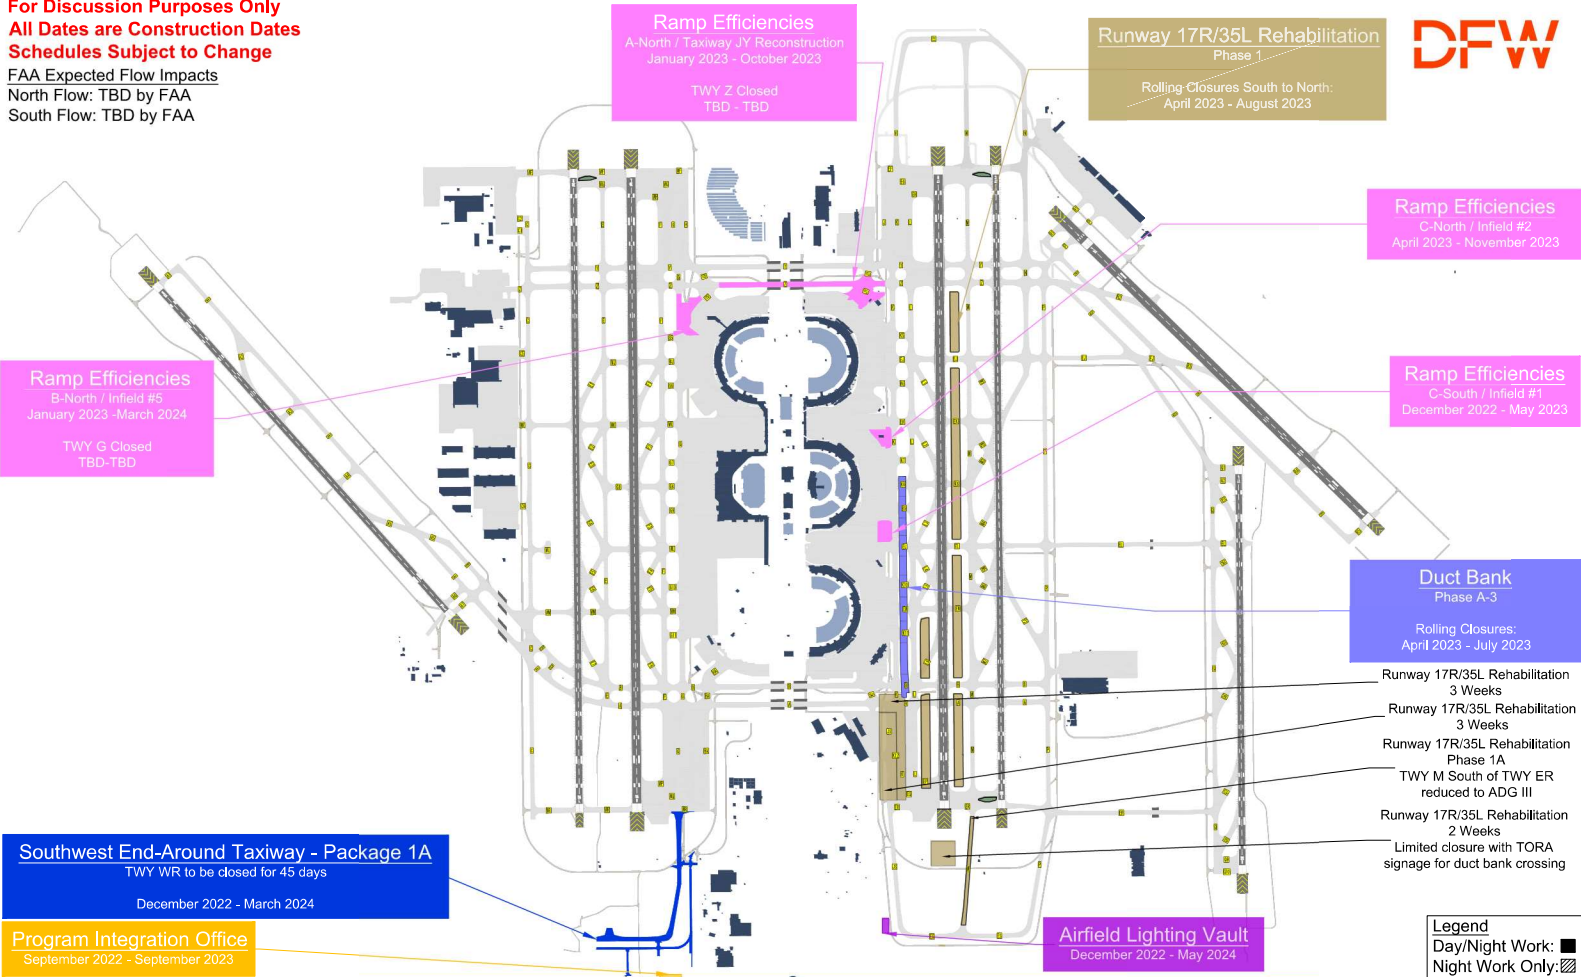

Legend	
Day/Night Work:	■
Night Work Only:	▨


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts

North Flow: TBD by FAA

South Flow: TBD by FAA

DFW

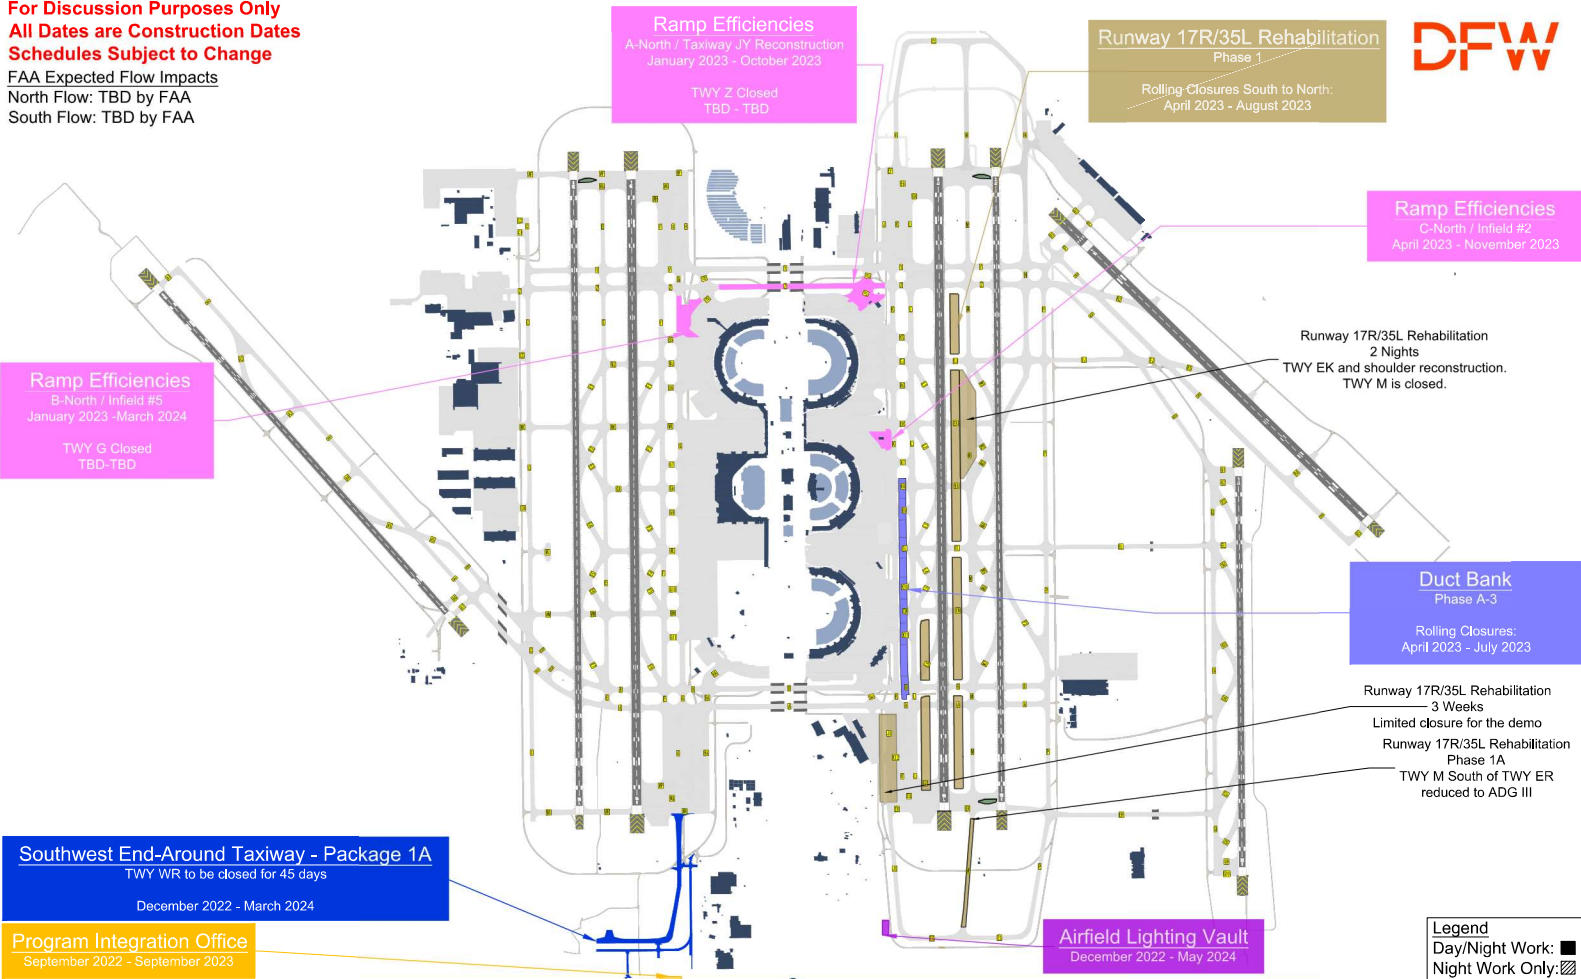


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts

North Flow: TBD by FAA

South Flow: TBD by FAA

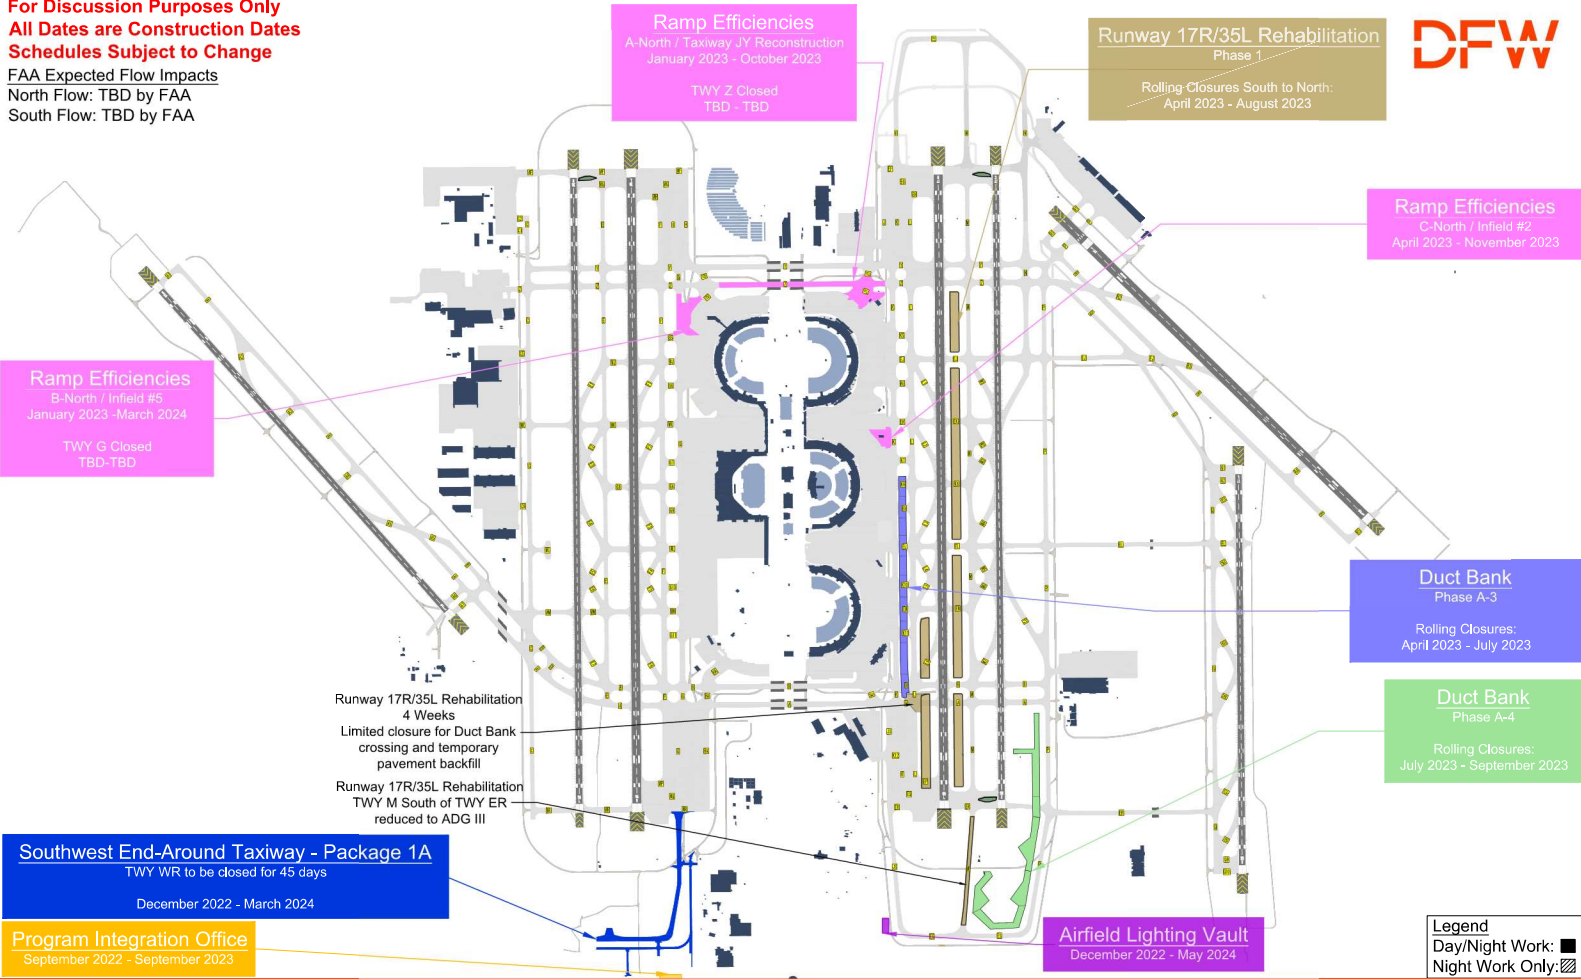


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts

North Flow: TBD by FAA

South Flow: TBD by FAA

DFW

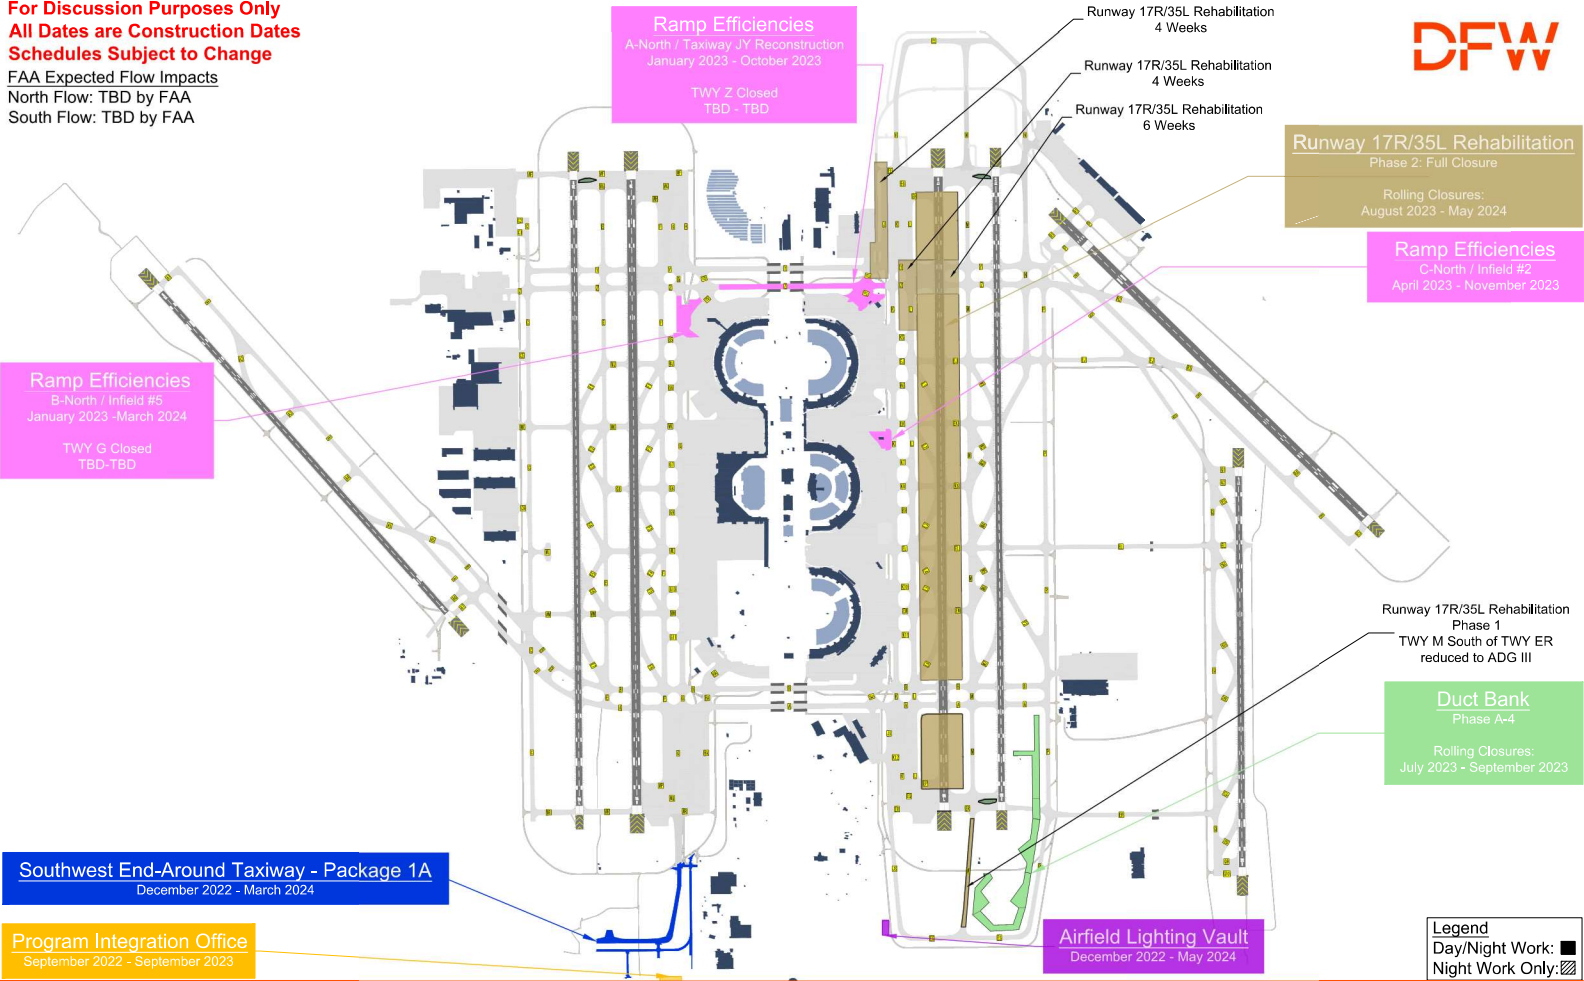


Legend

Day/Night Work: ■
Night Work Only: ▨

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change


FAA Expected Flow Impacts
 North Flow: TBD by FAA
 South Flow: TBD by FAA

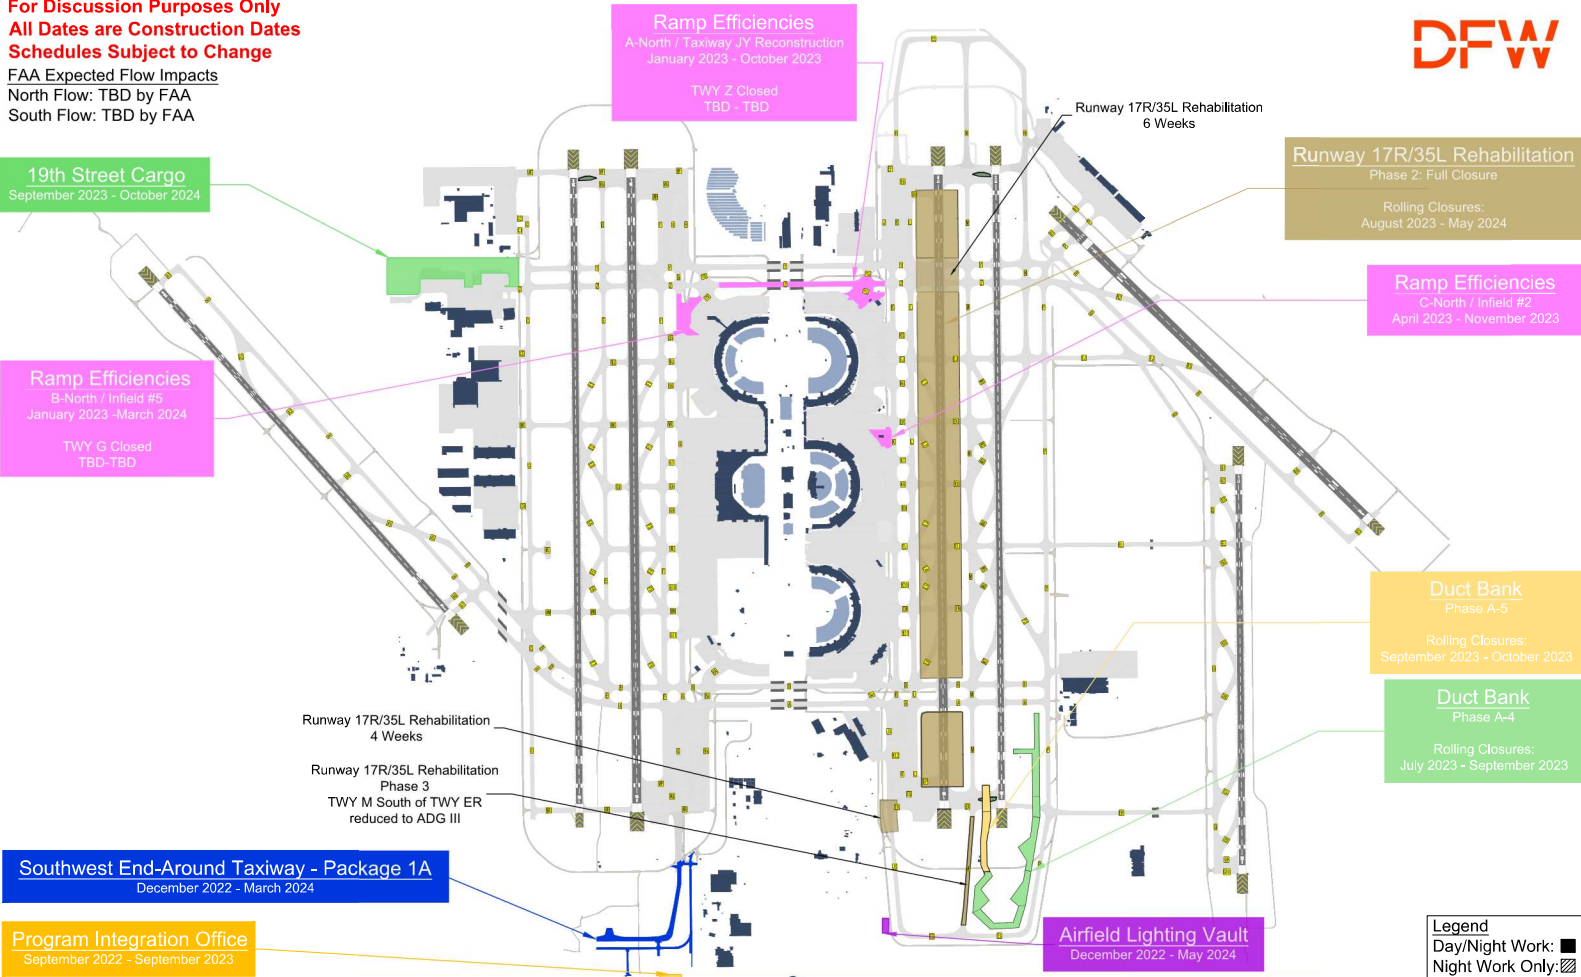

Legend	
Day/Night Work:	■
Night Work Only:	▨


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

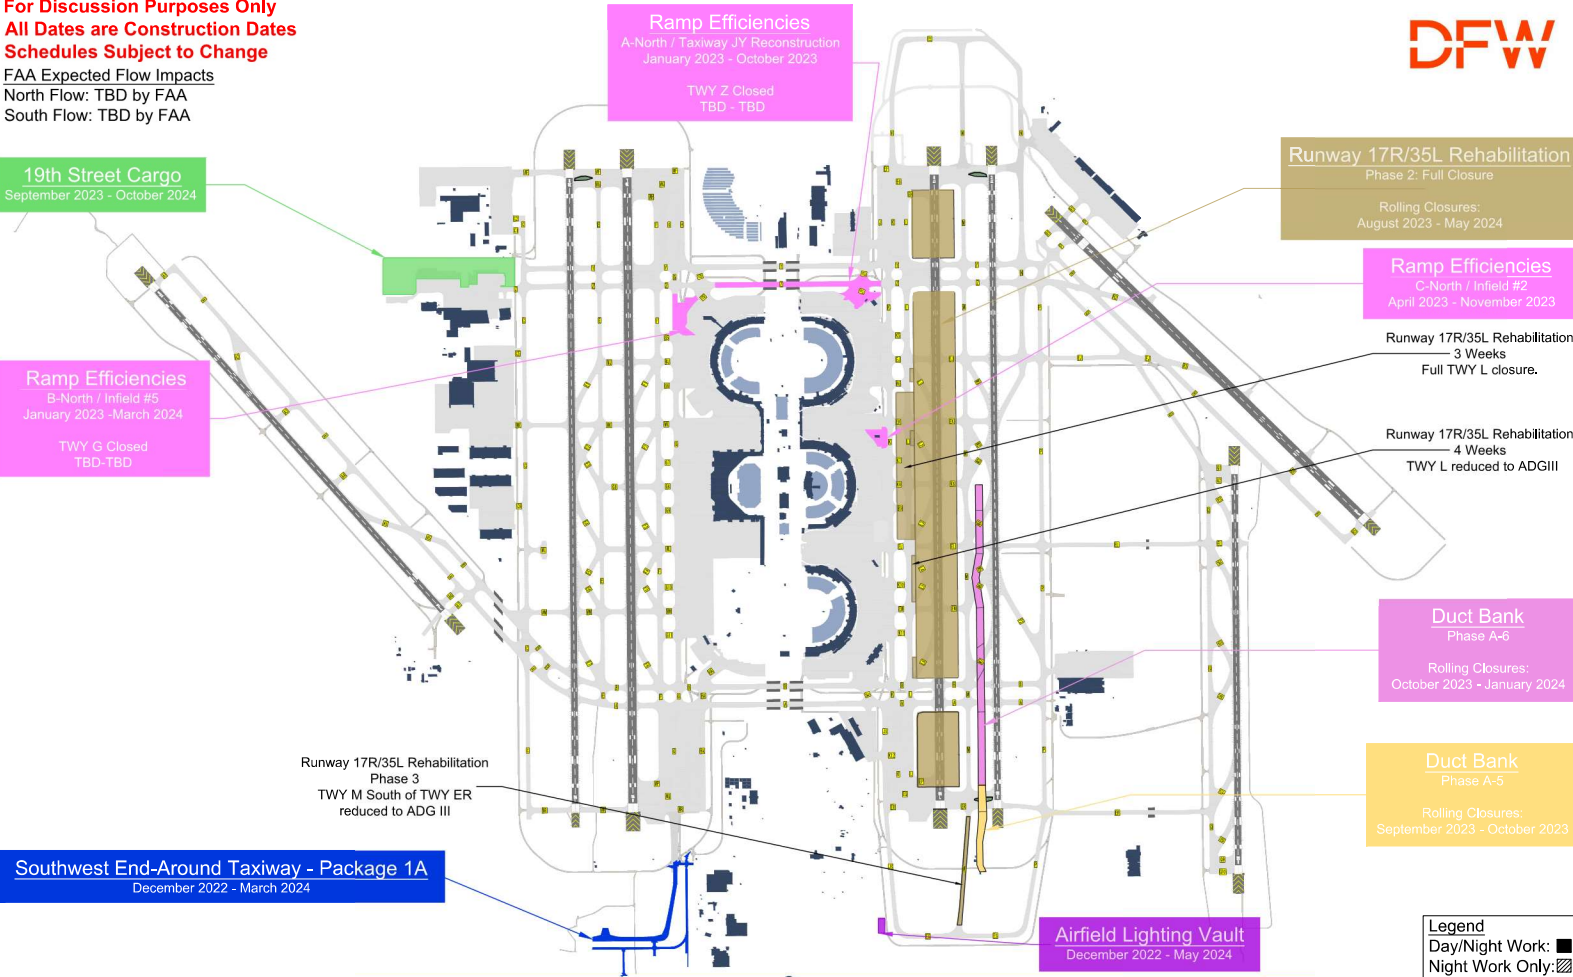

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change


FAA Expected Flow Impacts
 North Flow: TBD by FAA
 South Flow: TBD by FAA

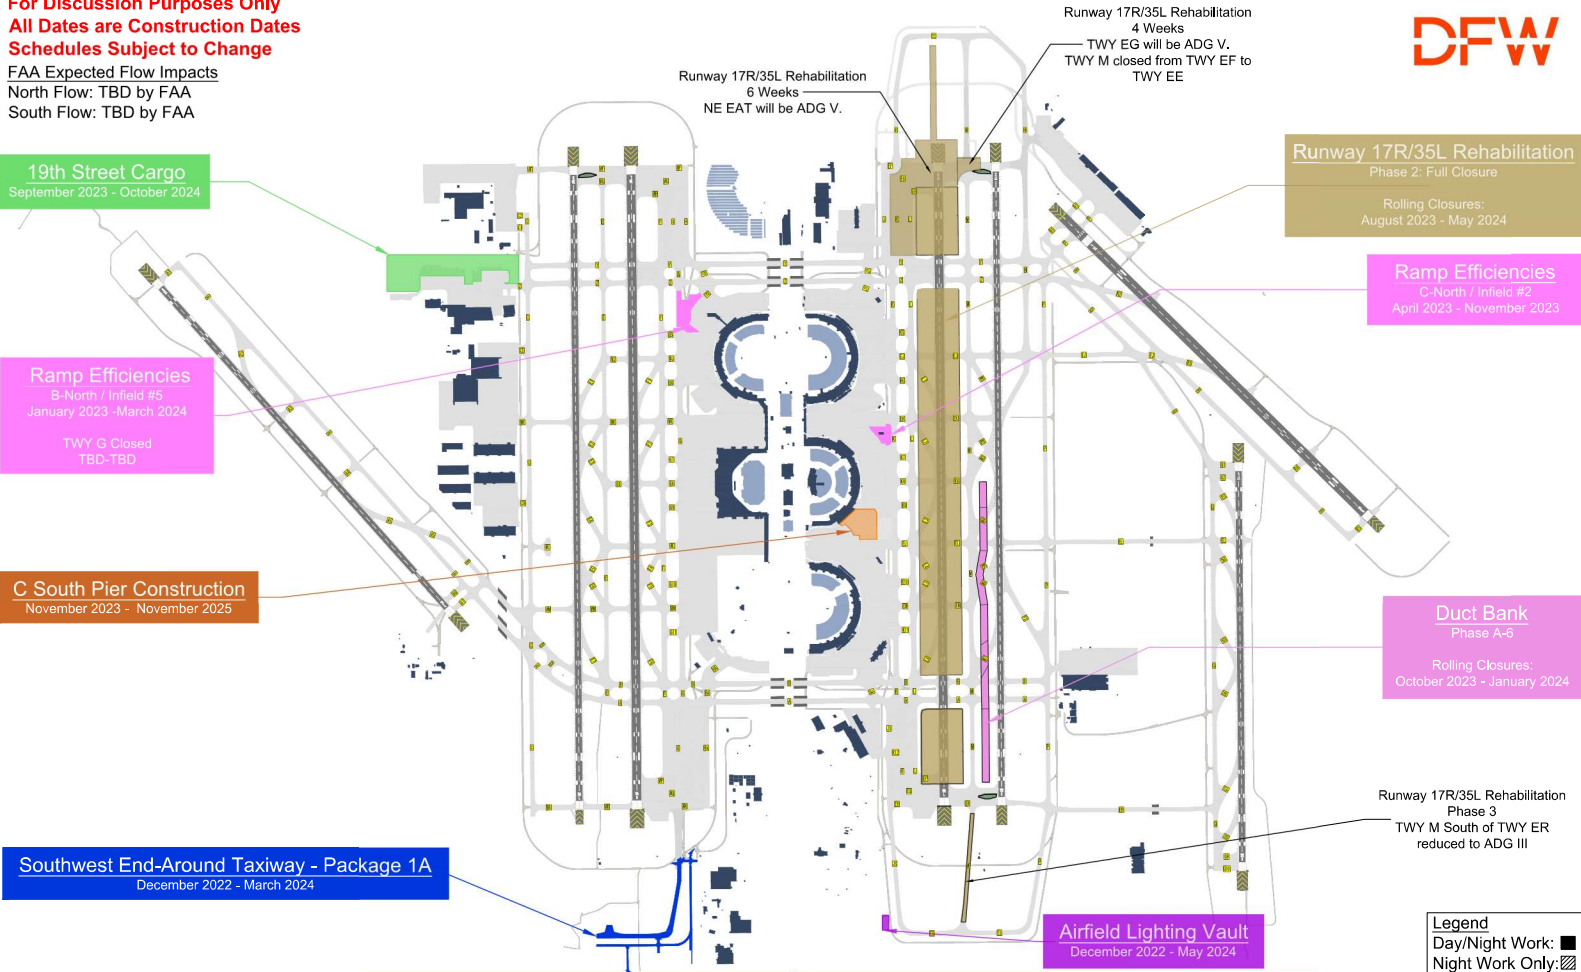

Legend	
Day/Night Work:	■
Night Work Only:	▨

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

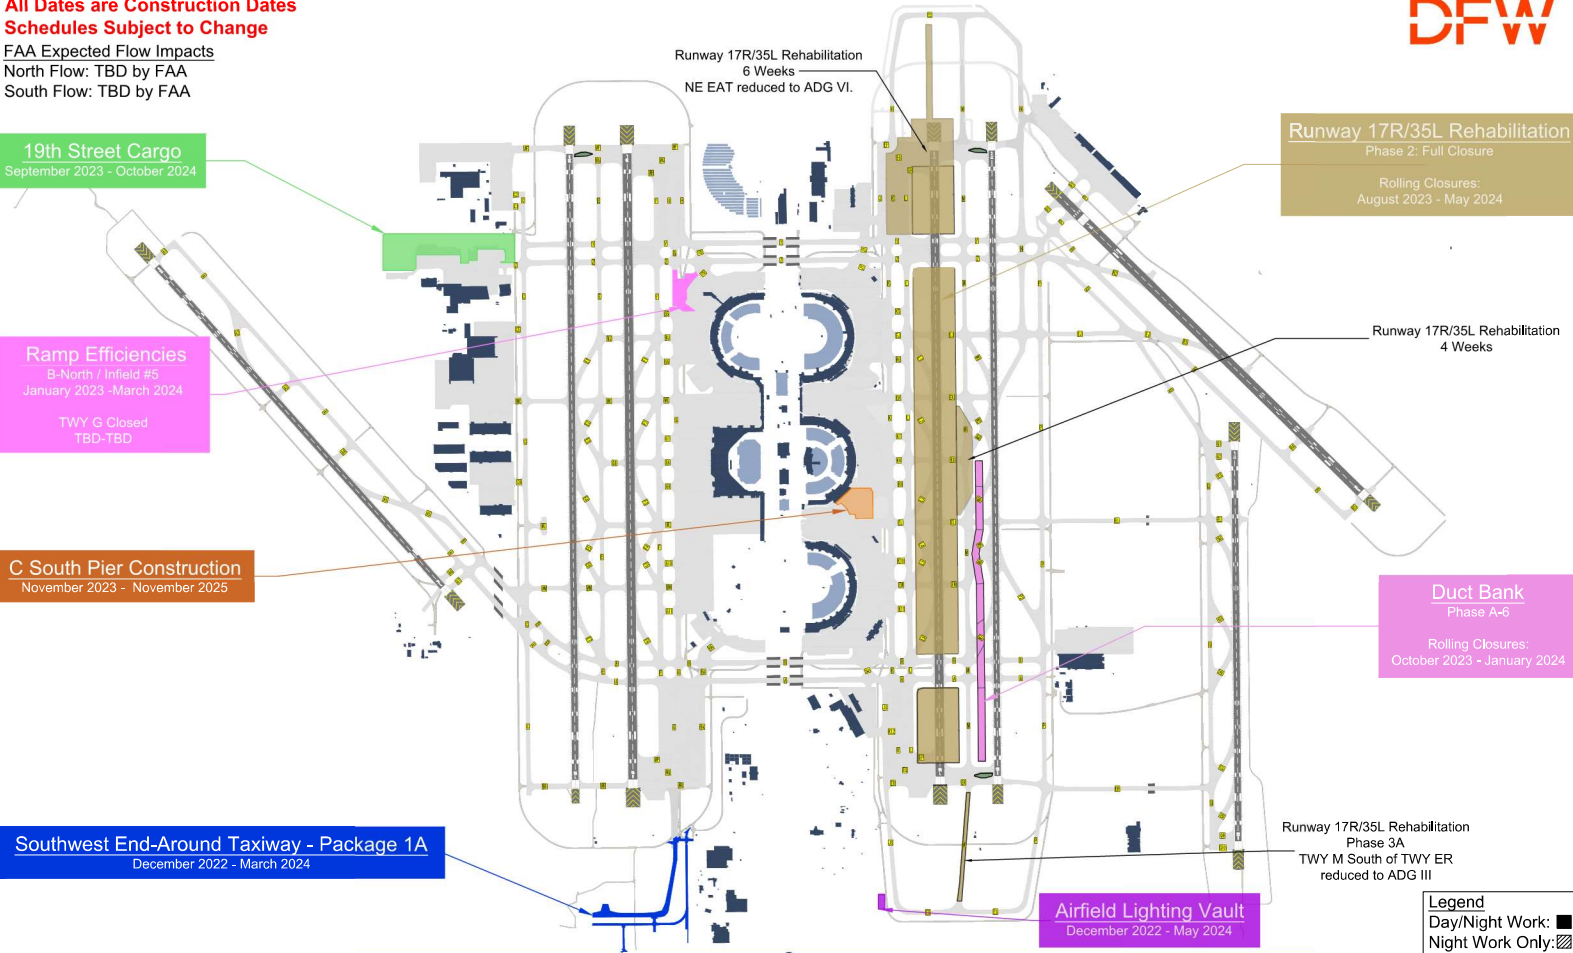

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts

North Flow: TBD by FAA

South Flow: TBD by FAA

DFW

19th Street Cargo
September 2023 - October 2024

A North Pier Construction
January 2024 - March 2026

Runway 17R/35L Rehabilitation
Phase 2: Full Closure
Rolling Closures:
August 2023 - May 2024

Ramp Efficiencies
B-North / Infield #5
January 2023 - March 2024
TWY G Closed
TBD-TBD

Duct Bank
Phase A-7
Rolling Closures:
January 2024 - February 2024

C South Pier Construction
November 2023 - November 2025

Duct Bank
Phase A-6
Rolling Closures:
October 2023 - January 2024

Southwest End-Around Taxiway - Package 1A
December 2022 - March 2024

Runway 17R/35L Rehabilitation
Phase 3A
TWY M South of TWY ER
reduced to ADG III

Airfield Lighting Vault
December 2022 - May 2024

Legend
Day/Night Work: ■
Night Work Only: ▨


↑ Date: January 6, 2023
Source: Dallas Fort Worth International Airport

Airfield Projects

FY2024 - January 2024 | page


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

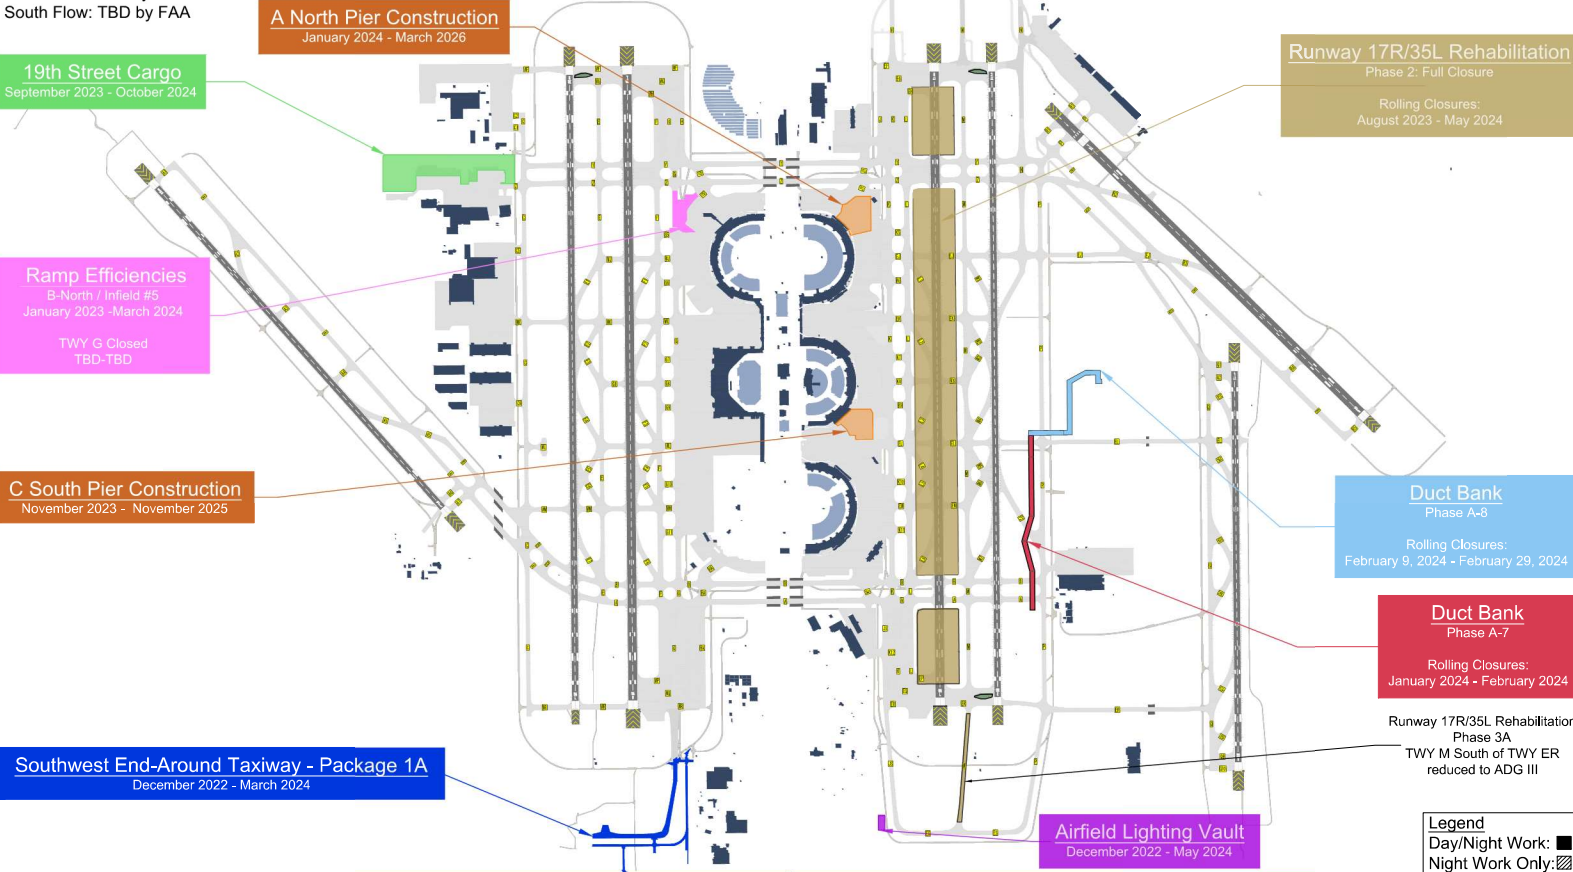

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

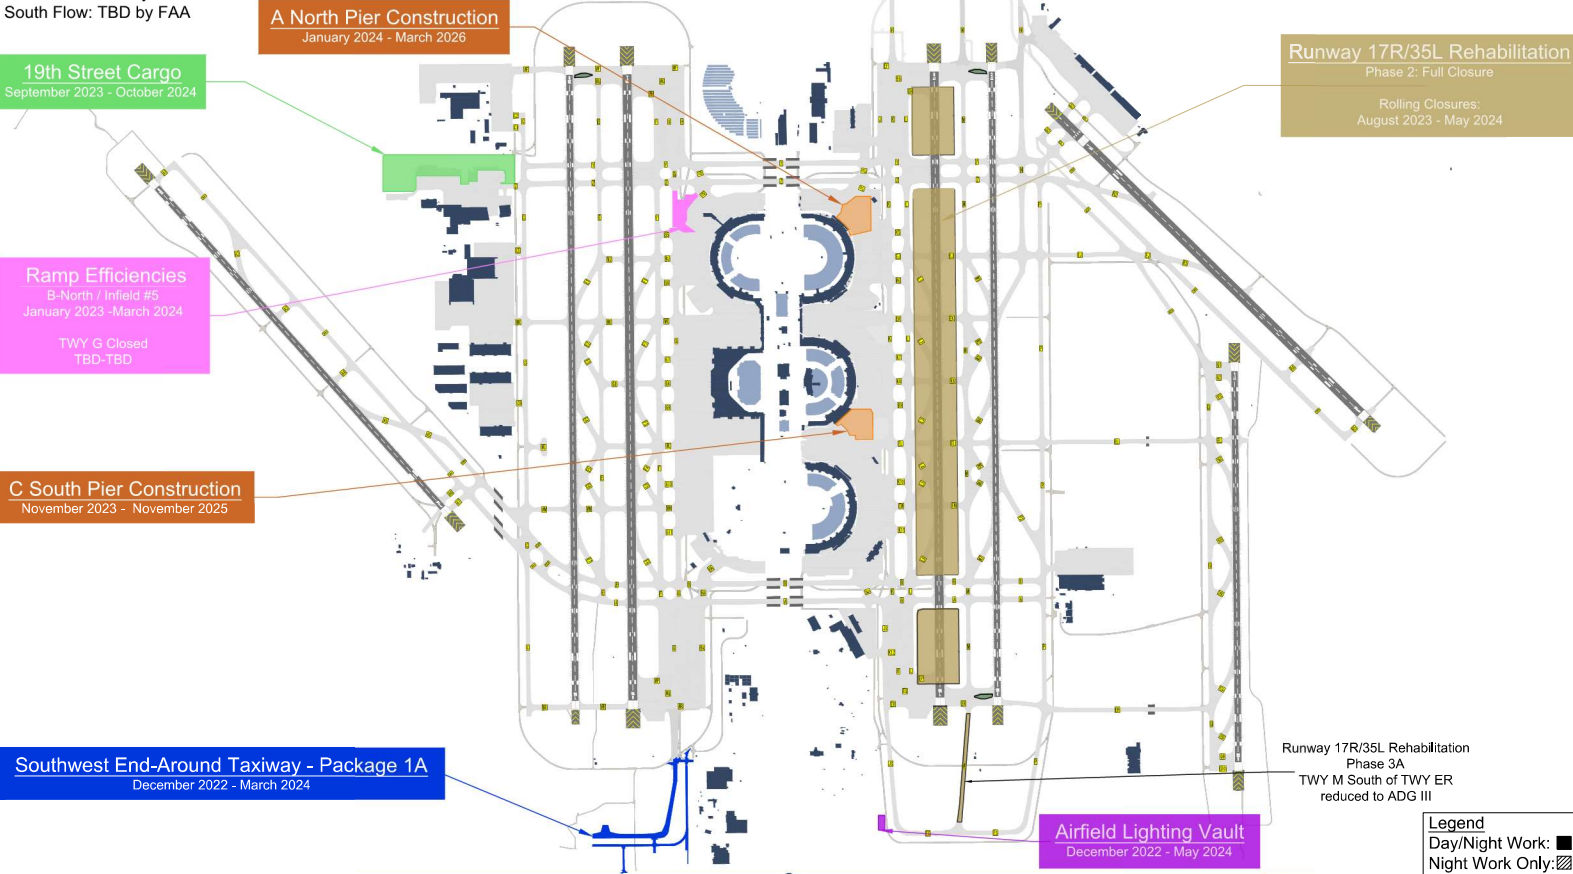

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA



19th Street Cargo
September 2023 - October 2024

A North Pier Construction
January 2024 - March 2026

Runway 17R/35L Rehabilitation
Phase 2: Full Closure
Rolling Closures:
August 2023 - May 2024

C South Pier Construction
November 2023 - November 2025


Airfield Lighting Vault
December 2022 - May 2024

Runway 17R/35L Rehabilitation
Phase 3A
TWY M South of TWY ER
reduced to ADG III

Legend
Day/Night Work: ■
Night Work Only: ▨

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

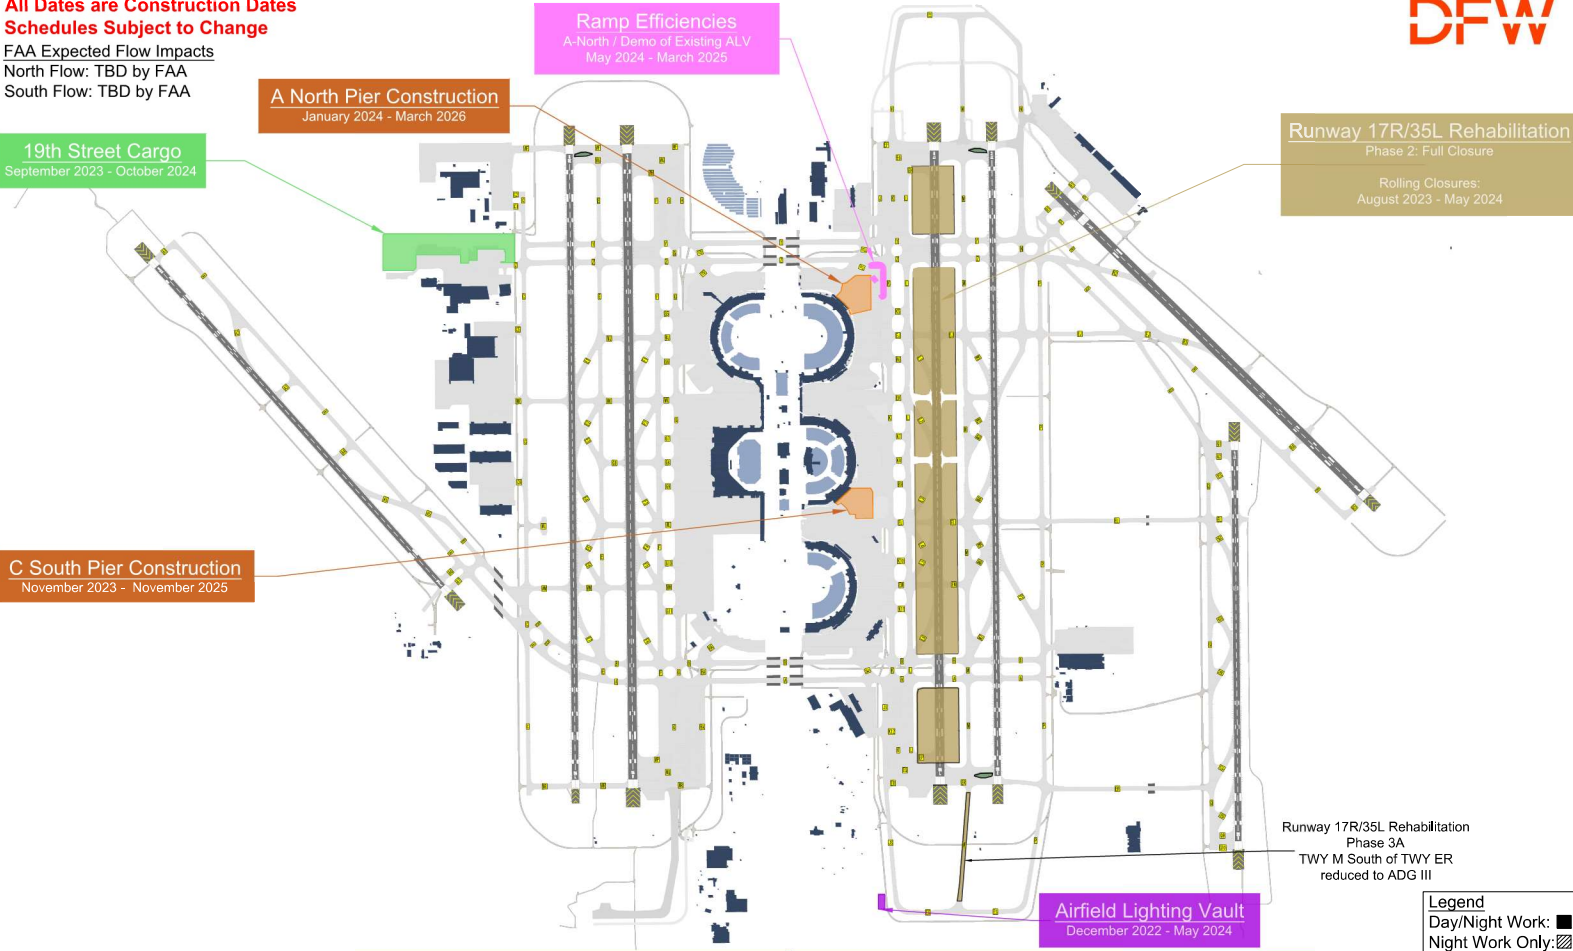

Legend
Day/Night Work: ■
Night Work Only: ▨

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

19th Street Cargo
September 2023 - October 2024

A North Pier Construction
January 2024 - March 2026

Ramp Efficiencies
A-North / Demo of Existing ALV
May 2024 - March 2025

C South Pier Construction
November 2023 - November 2025

Runway 17R/35L Rehabilitation
South Runway End-Phase 3

Rolling Closures:
June 2024 - October 2024

Runway 17R/35L Rehabilitation
Phase 2A
RW 17R/35L threshold relocated to TWY EM.
TWY M South of TWY ER reduced to ADG III

Legend
Day/Night Work: ■
Night Work Only: ▨

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

19th Street Cargo
September 2023 - October 2024

A North Pier Construction
January 2024 - March 2026

Ramp Efficiencies
A-North / Demo of Existing ALV
May 2024 - March 2025

C South Pier Construction
November 2023 - November 2025

Runway 17R/35L Rehabilitation
South Runway End-Phase 3

Rolling Closures:
June 2024 - October 2024

Runway 17R/35L Rehabilitation
Phase 2A
RW 17R/35L threshold relocated to TWY EM.
TWY M South of TWY ER reduced to ADG III

Legend
Day/Night Work: ■
Night Work Only: ▨

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change


FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

19th Street Cargo
September 2023 - October 2024

A North Pier Construction
January 2024 - March 2026


Ramp Efficiencies
A-North / Demo of Existing ALV
May 2024 - March 2025

C South Pier Construction
November 2023 - November 2025

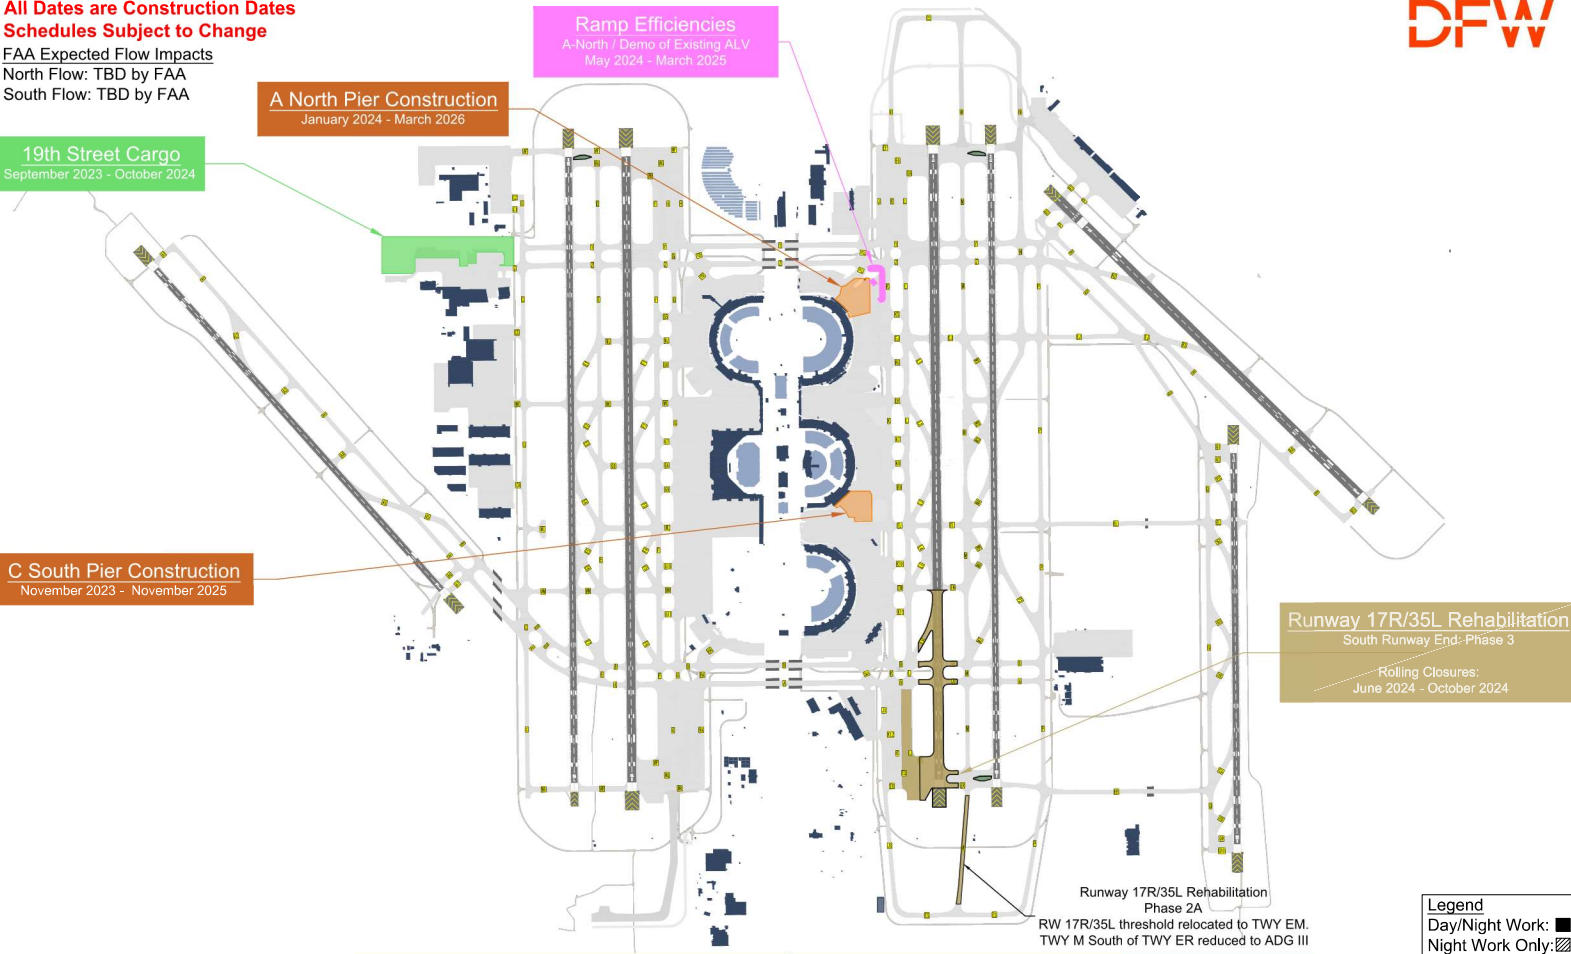


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

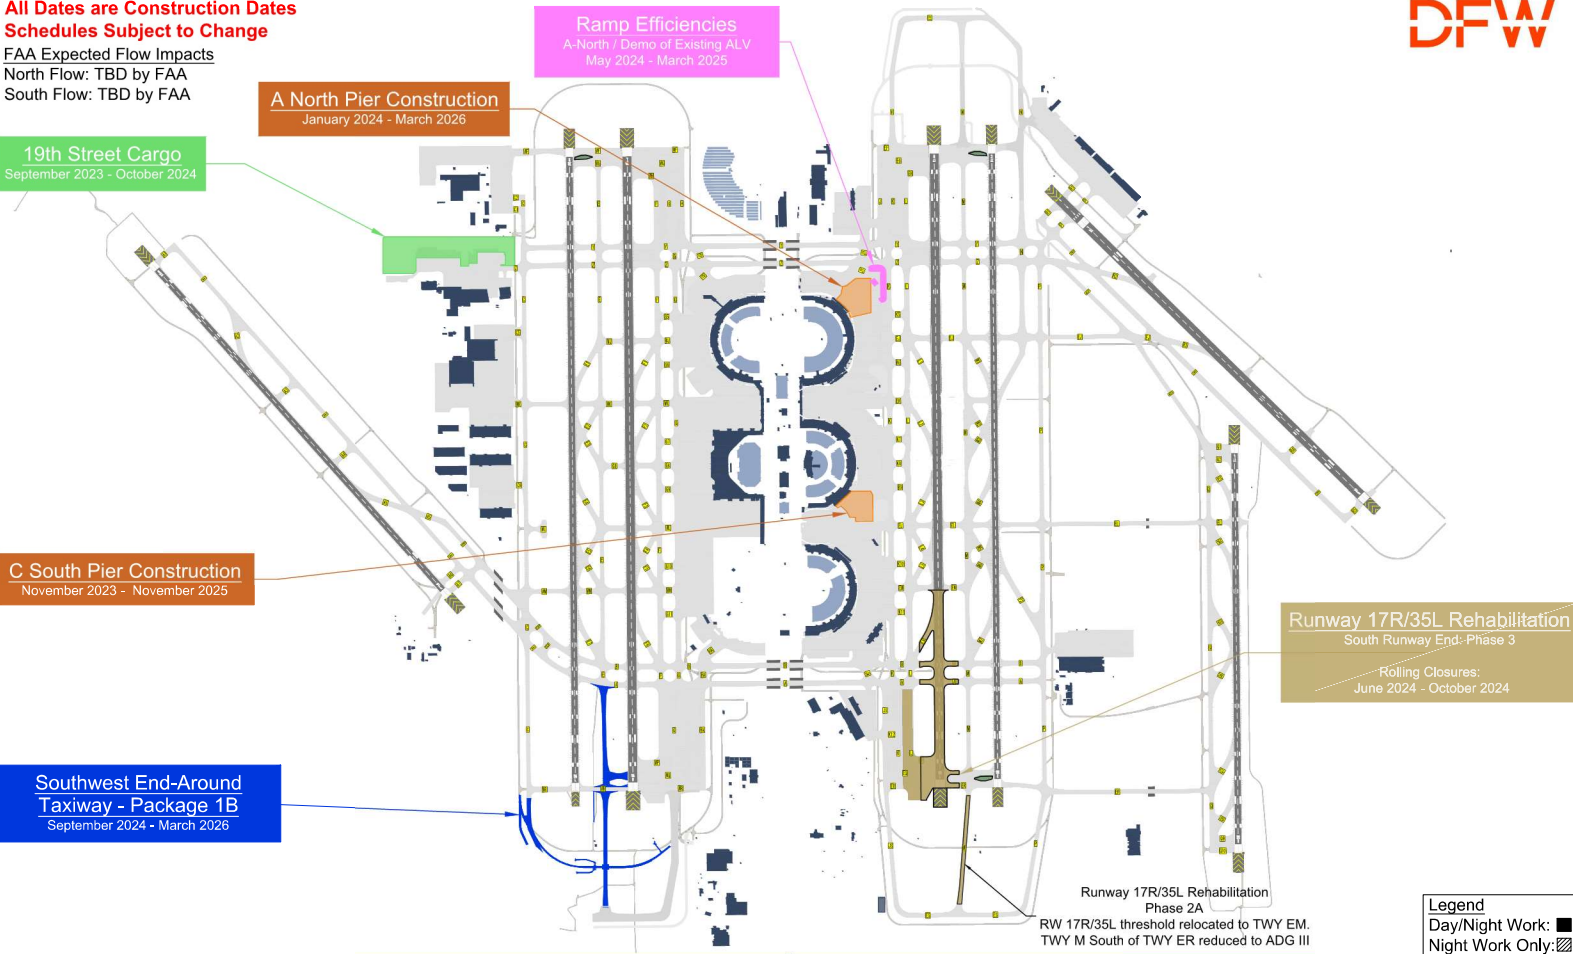

Legend
Day/Night Work: ■
Night Work Only: ▨


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change
FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

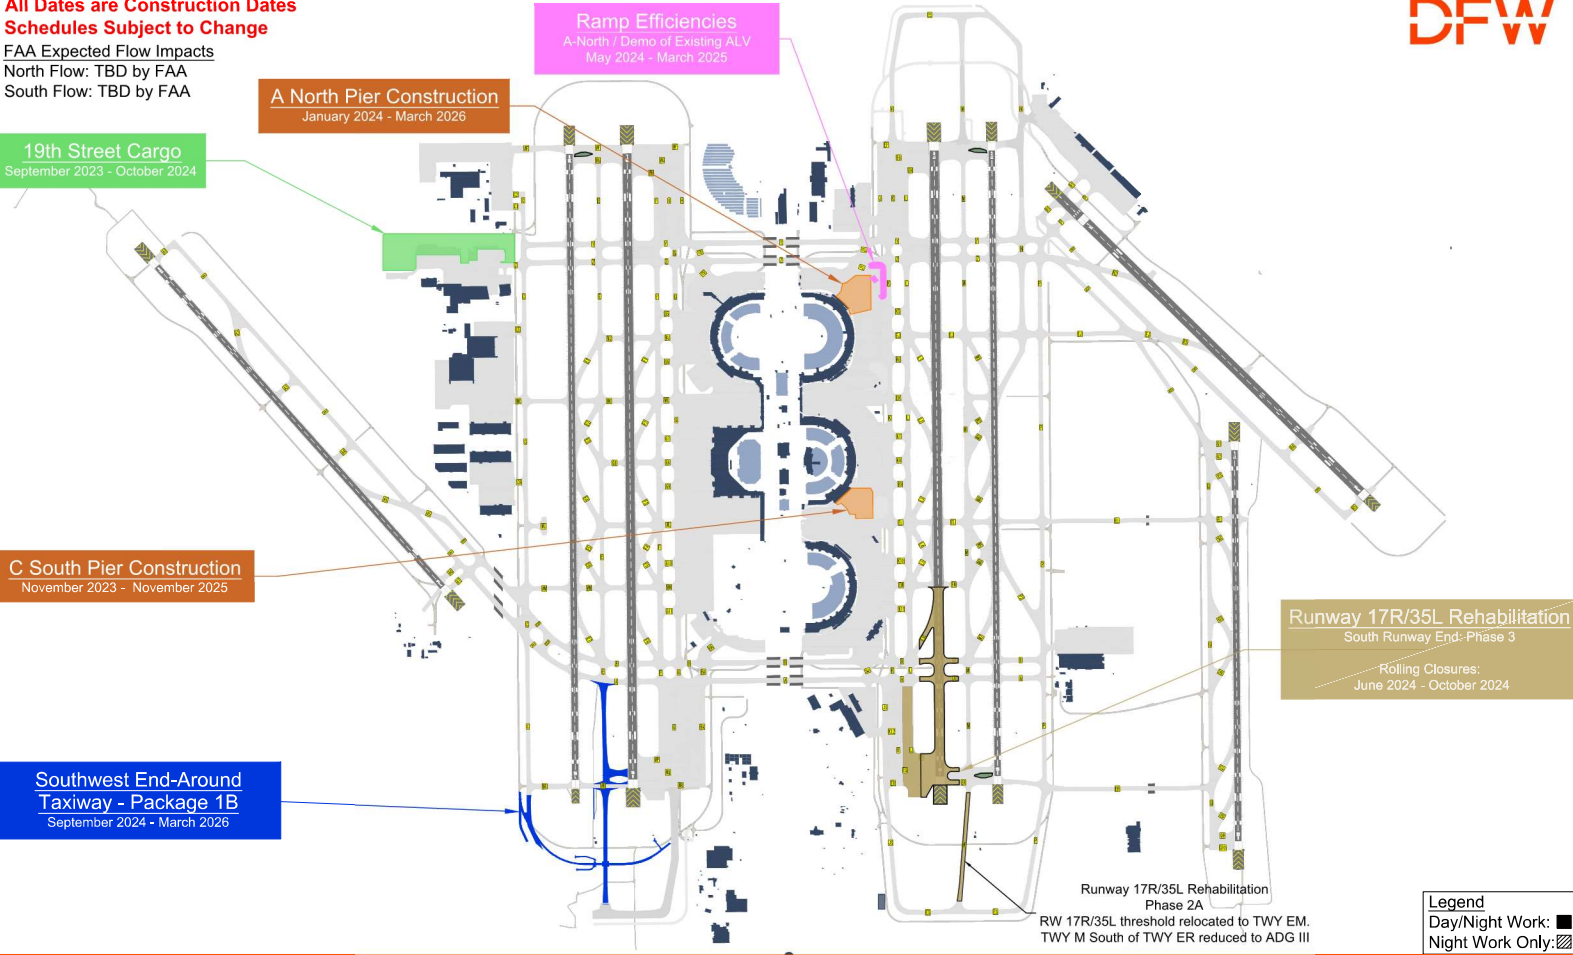

Legend
Day/Night Work: ■
Night Work Only: ▨


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

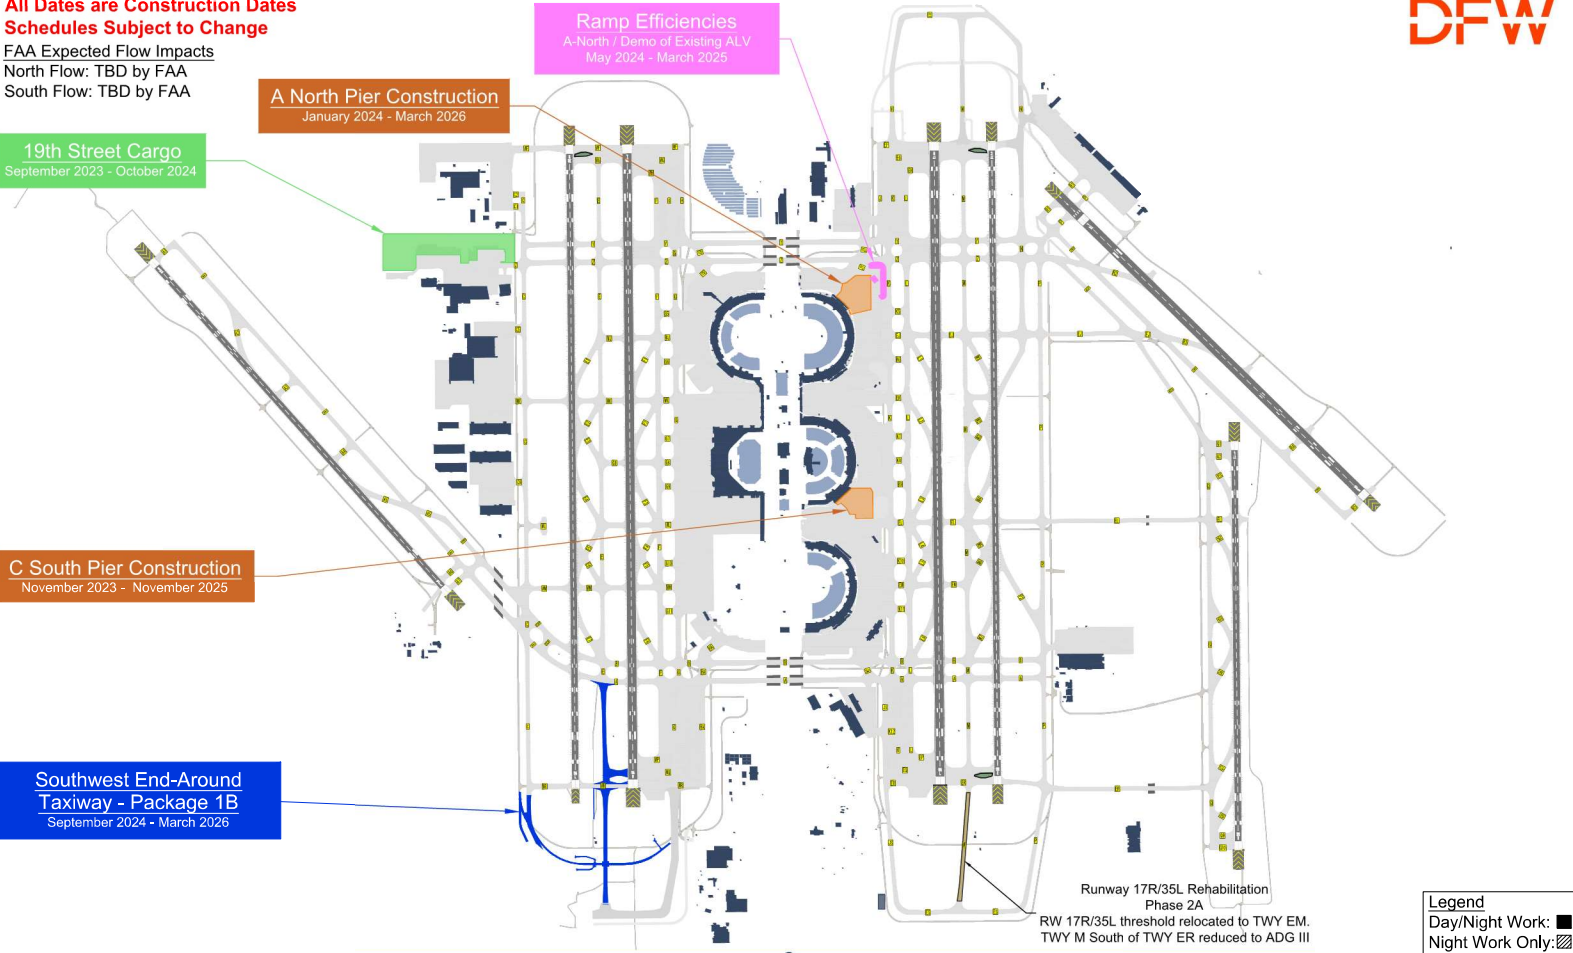


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change


FAA Expected Flow Impacts
North Flow: TBD by FAA
South Flow: TBD by FAA

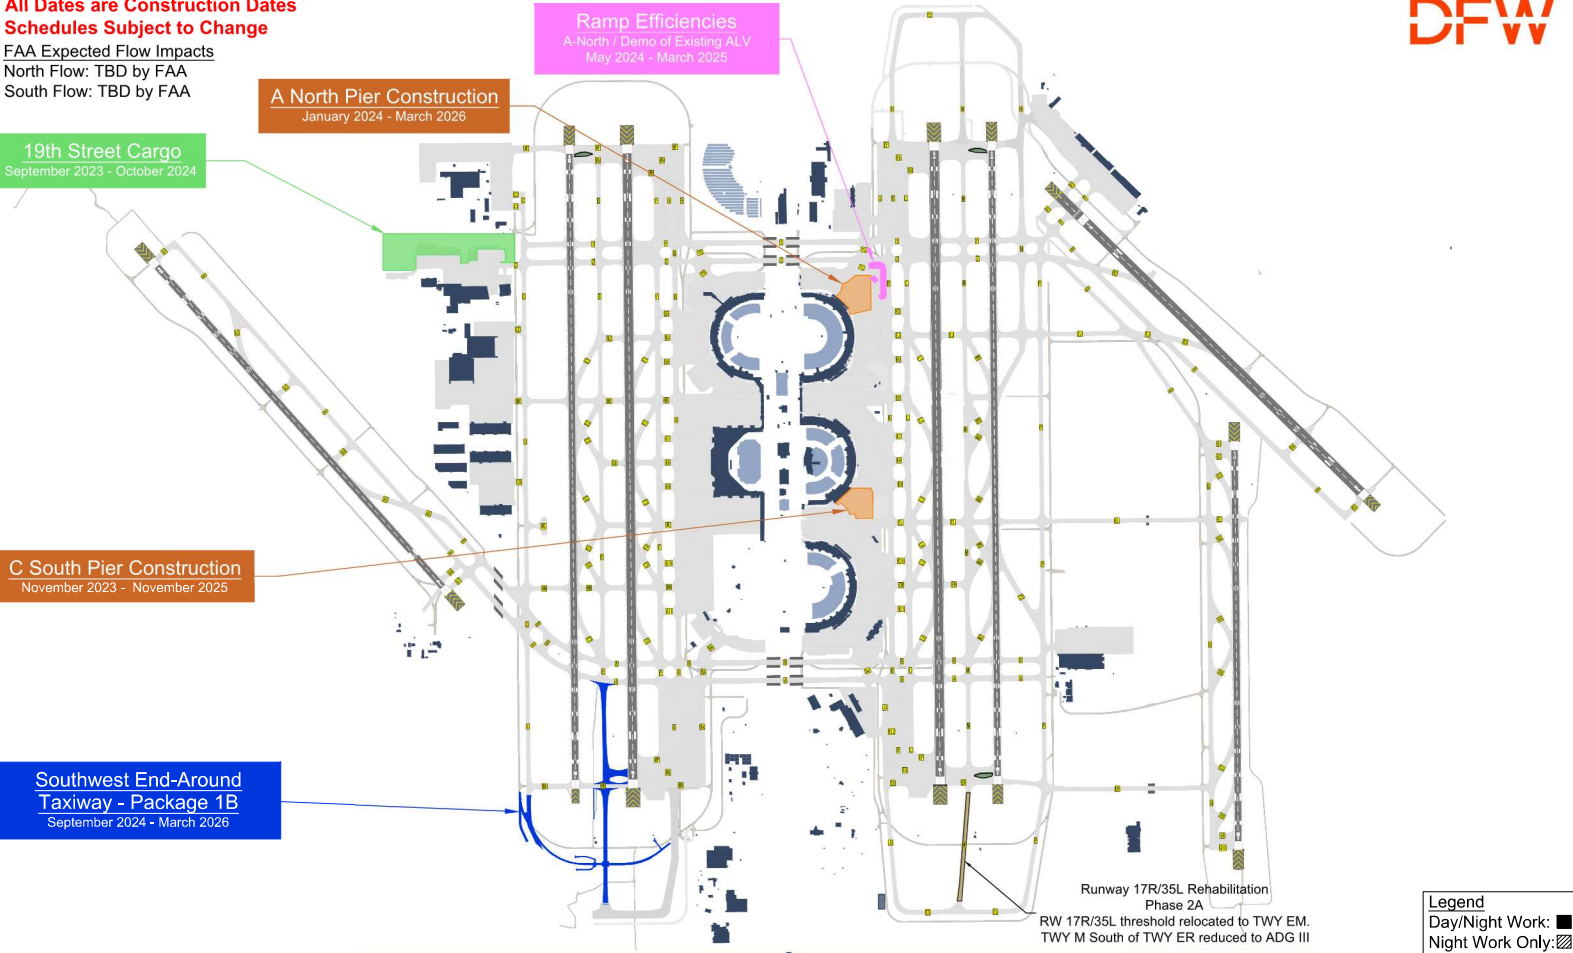


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

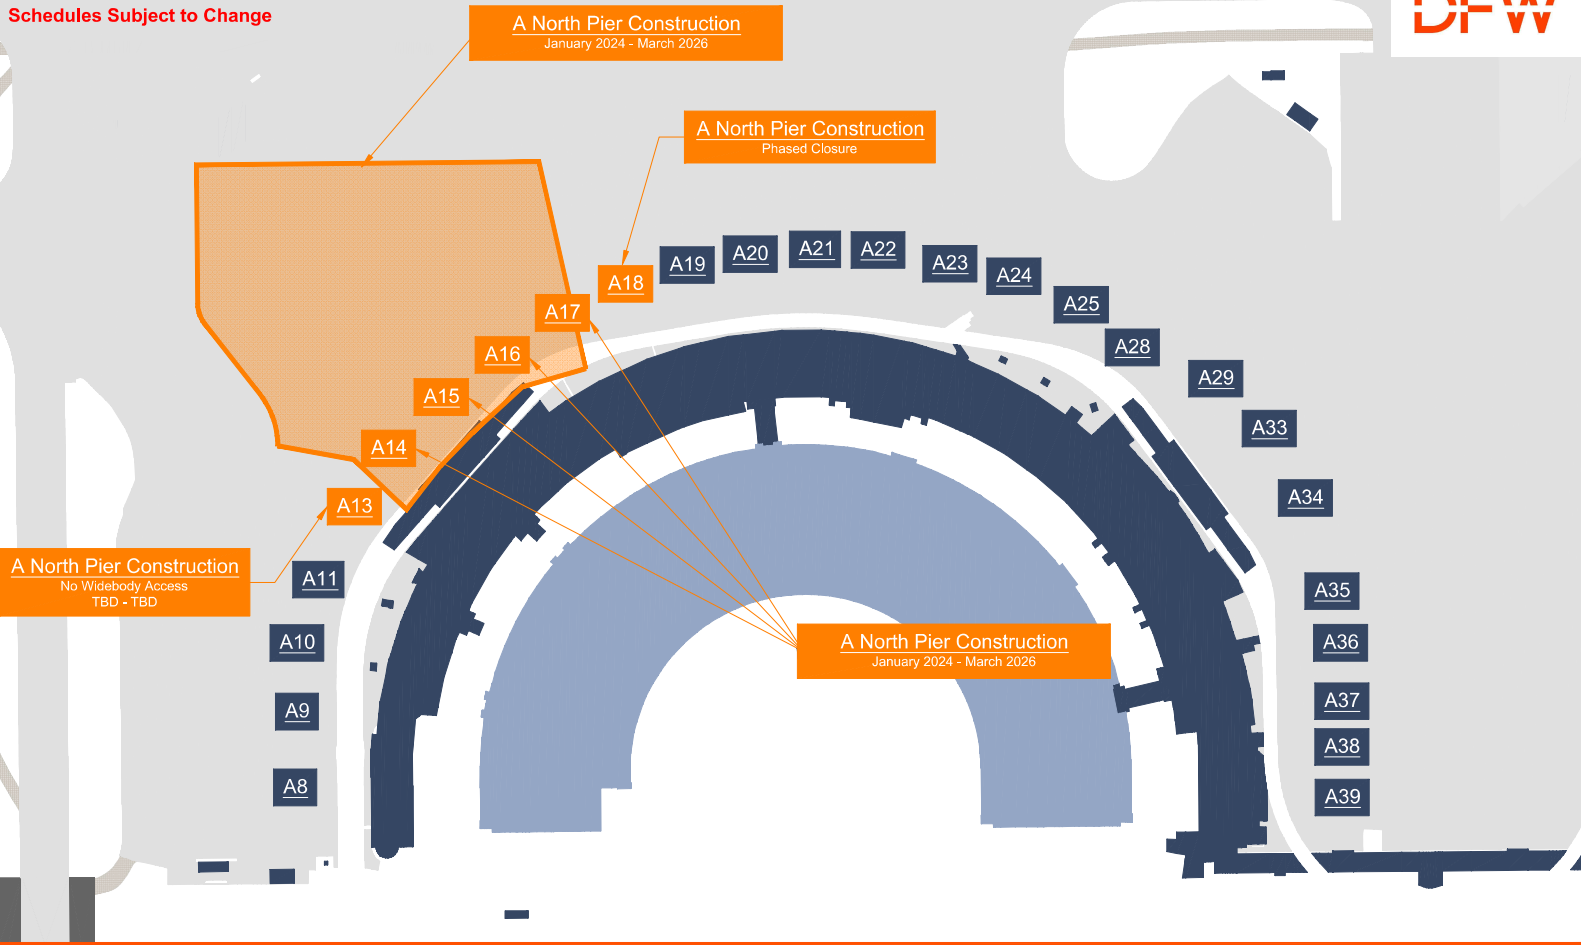


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

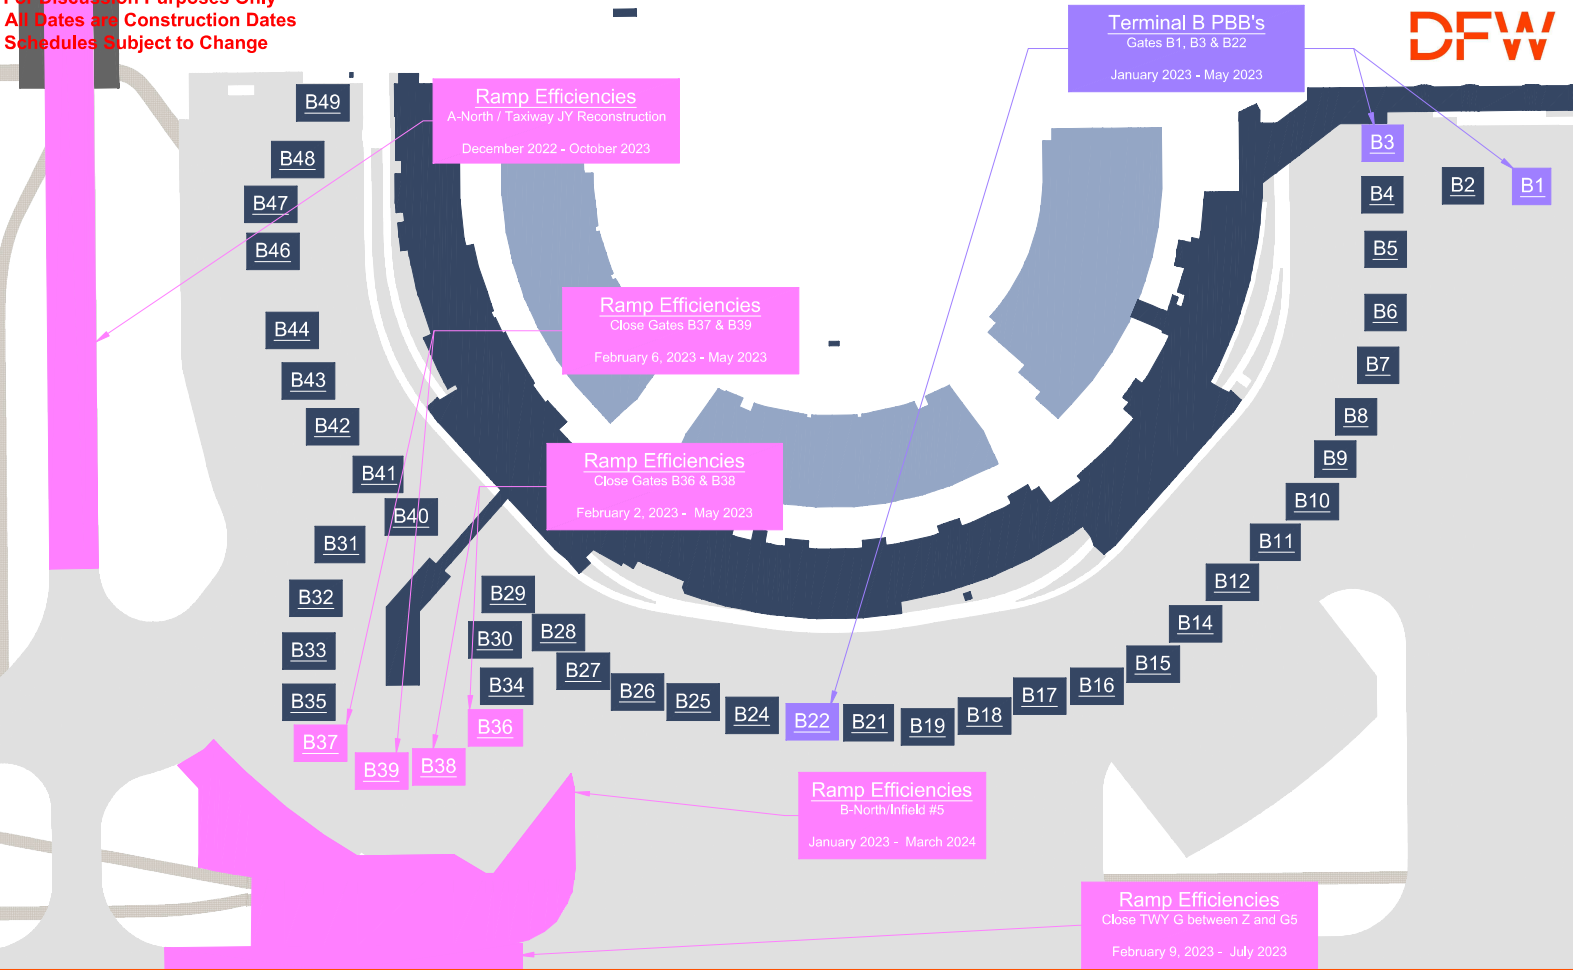


DFW

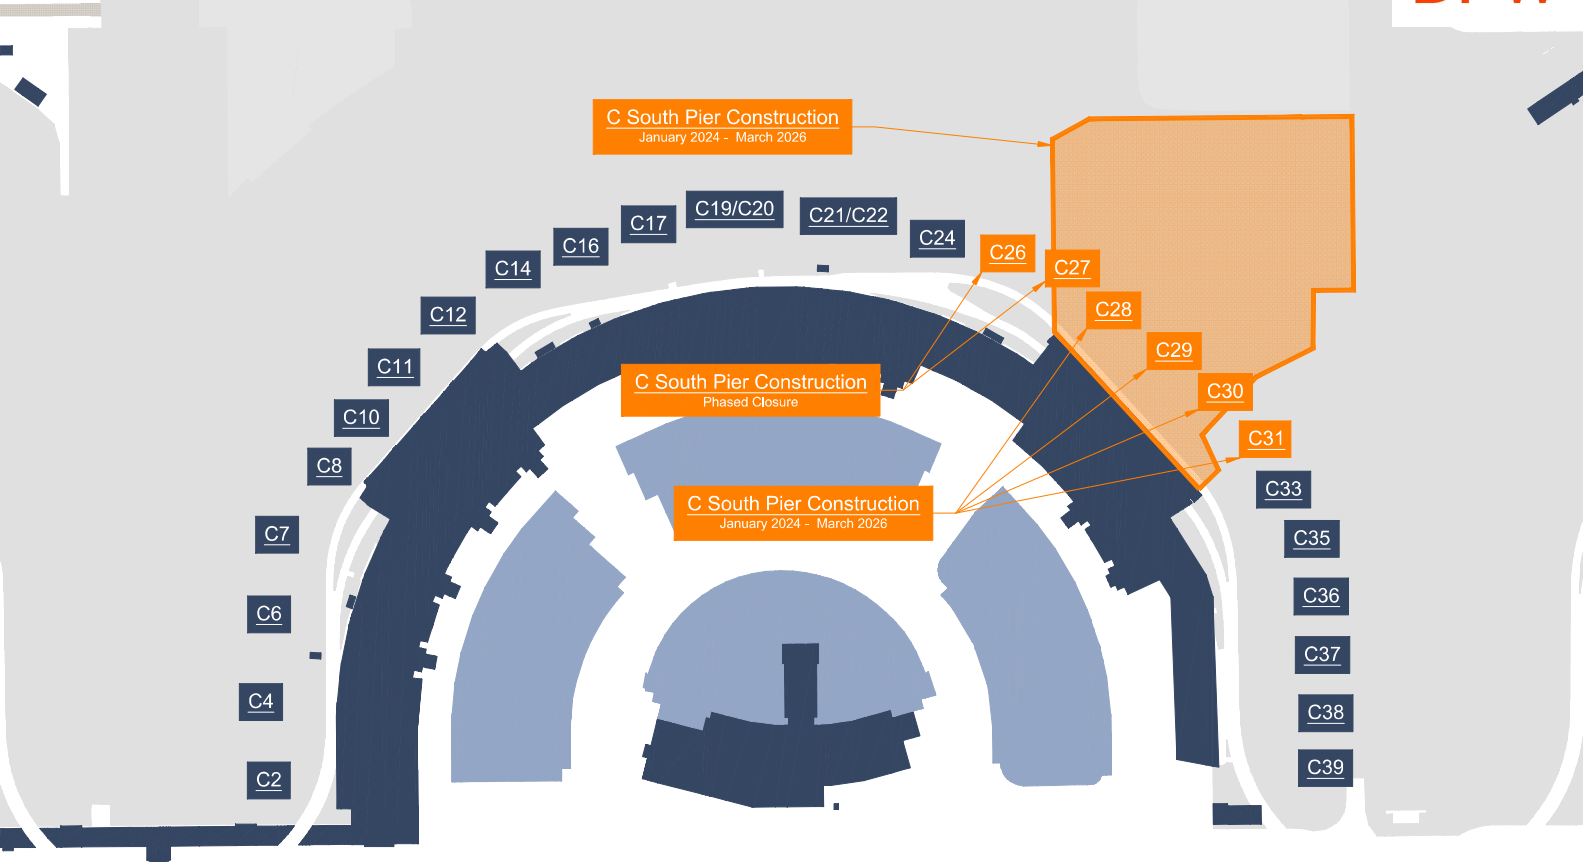

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

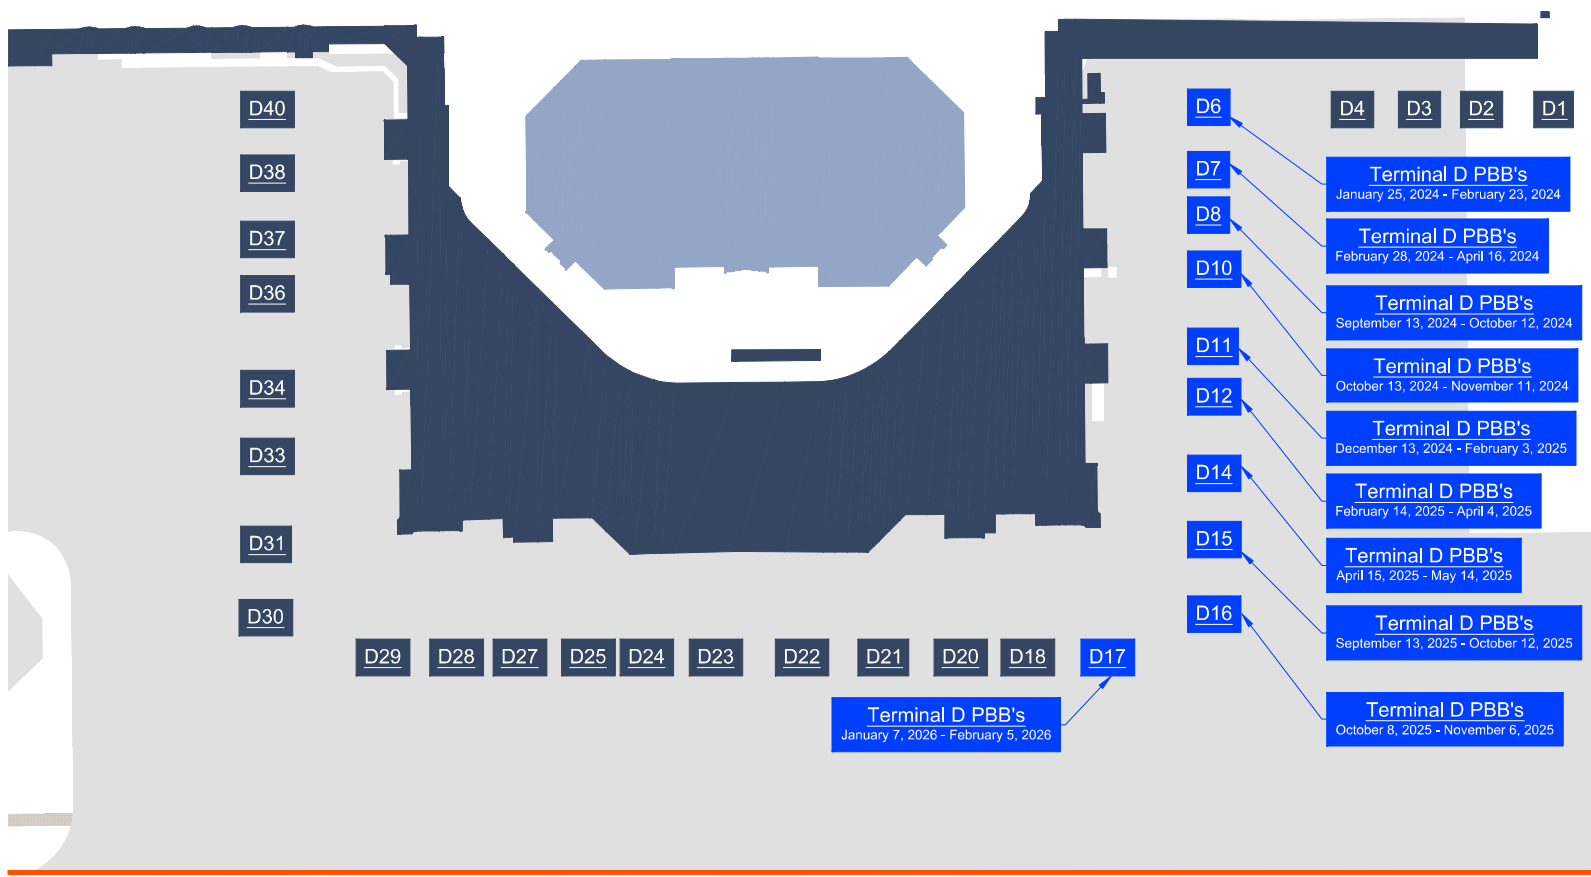

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

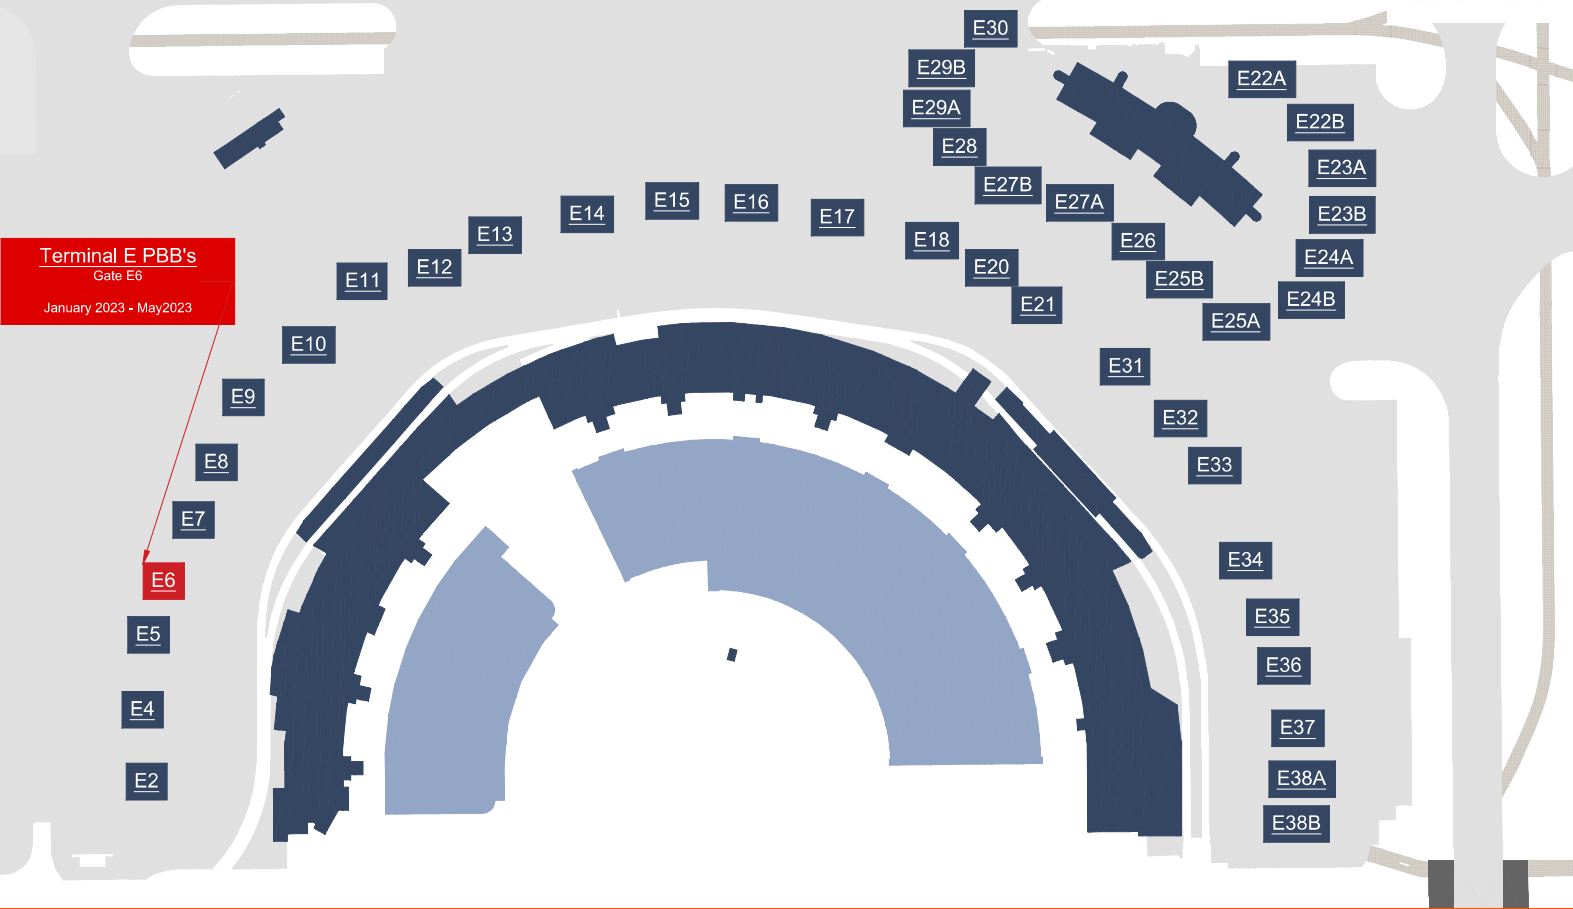

Appendix


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change



APPROVED PROJECT AREA			
Number	Permit #	Project Code	Project Name & Dates
1 ^A	A22-068B	NCOM-040	19th St Redevelopment April 2023 - September 2024
3	XXX	XXX-XXX	Terminal A Roofing Project MM/YYYY - MM/YYYY
4	In Project Area ^C	TFD-004	CTA Expansion Pier A March 2023 - November 2025
5	In Project Area ^C	AFD-NEW	Terminal C Renovation Phase 3 MM/YYYY - MM/YYYY
6	A21-136	XXX-XXX	AA PCA Project - Terminal D MM/YYYY - November 2023
7	In Project Area ^C	AFD-NEW	Terminal C Renovation Phase 2 MM/YYYY - MM/YYYY
8	XXX-XXX	NSAF-076	West ARFF Projects May 2023 - February 2025
9	In Project Area ^C	TFD-003	CTA Expansion Pier C Phase 1A March 2023 - November 2025
9	In Project Area ^C	XXX-XXX	CTA Expansion Pier C Phase 1B MM/YYYY - MM/YYYY
10	XXX-XXX	NSAF-076	East ARFF Projects December 2022 - February 2025
11	A21-263B	SAF-007	AGA Gate Replacement April 2022 - July 2023
12	XXX-XXX	TFD-003	CTA Expansion Pier C March 2023 - November 2025
13	A22-003B	AFD-141	Airfield Pavement Remediation Pkg 1 July 2022 - March 2023
14	A21-401B	TER-274	PBB Replacement Program 1 January 2023 - June 2023
15 ^A	XXX-XXX	TFD-002	Ramp Efficiencies Package 2 October 2022 - December 2024
16 ^A	XXX	TFD-001	Ramp Efficiencies Package 1 July 2022 - December 2025
17	XXX-XXX	TFD-004	CTA Expansion Pier A March 2023 - November 2025
18 ^A	XXX-XXX	TFD-001	Terminal C Garage March 2023 - May 2027
19 ^A	XXX-XXX	AFD-065-B	17R/3SL Rehabilitation January 2023 - October 2024
23 ^A	XXX-XXX	AFD-048	SW EAT Packages 1A December 2022 - December 2023
24	A22-072B	TFD-011	CTA Expansion PIO October 2022 - December 2023
25	A19-271 A21-272B A19-273B	TER 180	CTX Recap Term A, B, & C March 2022 - January 2026
26	XXX	TFD-008	Service Delivery System May 2023 - October 2024
27	A21-137	XXX-XXX	AA PCA Project - Terminal D MM/YYYY - November 2023
30	A22-114B	TDF-001	Ramp Efficiencies Package 1 - Vault July 2022 - December 2025
31	A21-126B	XXX-XXX	Soil Slope Remediation July 2022 - February 2023
32	XXX-XXX	XXX-XXX	Future Development MM/YYYY - MM/YYYY
33/33 ^C	In Project Area ^C	XXX-XXX	ECUP Lay Down Area March 2023 - December 2024
34	A21-169B, A21-170B, A21-172B, A21-173B, A21-262B	XXX-XXX	Overhead Vertical Height Clear Sign May 2022 - MM/YYYY

REJECTED PROJECT AREA			
Number	Acreage	Project Code	Project Name & Dates
21 ^A	2.79	RDS-067	IP RightNADB/HML March 2022 - December 2025
22	XXX-XXX	TER 180-A	CTX Recap Term D September 2022 - February 2026


PROPOSED PROJECT AREA			
Number	Acreage	Project Code	Project Name & Dates
28 ^A	2.47	RDS-067	IP RightNADB/HML MM/YYYY - MM/YYYY
29 ^A	2.00	RDS-067	IP RightNADB/HML MM/YYYY - MM/YYYY

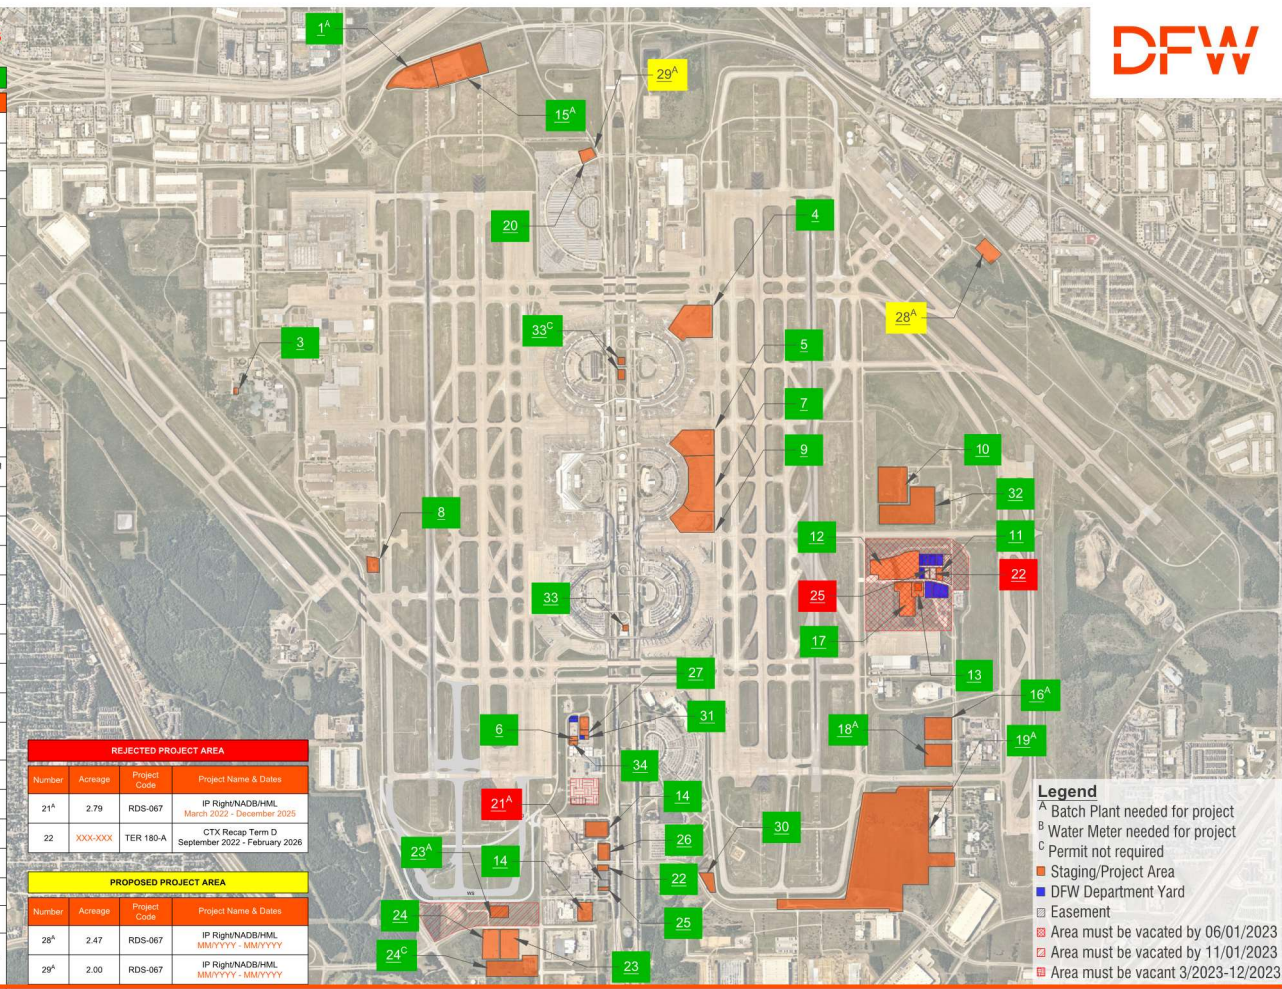


- Legend**
- ^A Batch Plant needed for project
 - ^B Water Meter needed for project
 - ^C Permit not required
 - Staging/Project Area
 - DFW Department Yard
 - Easement
 - Area must be vacated by 06/01/2023
 - Area must be vacated by 11/01/2023
 - Area must be vacant 3/2023-12/2023


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

DFW

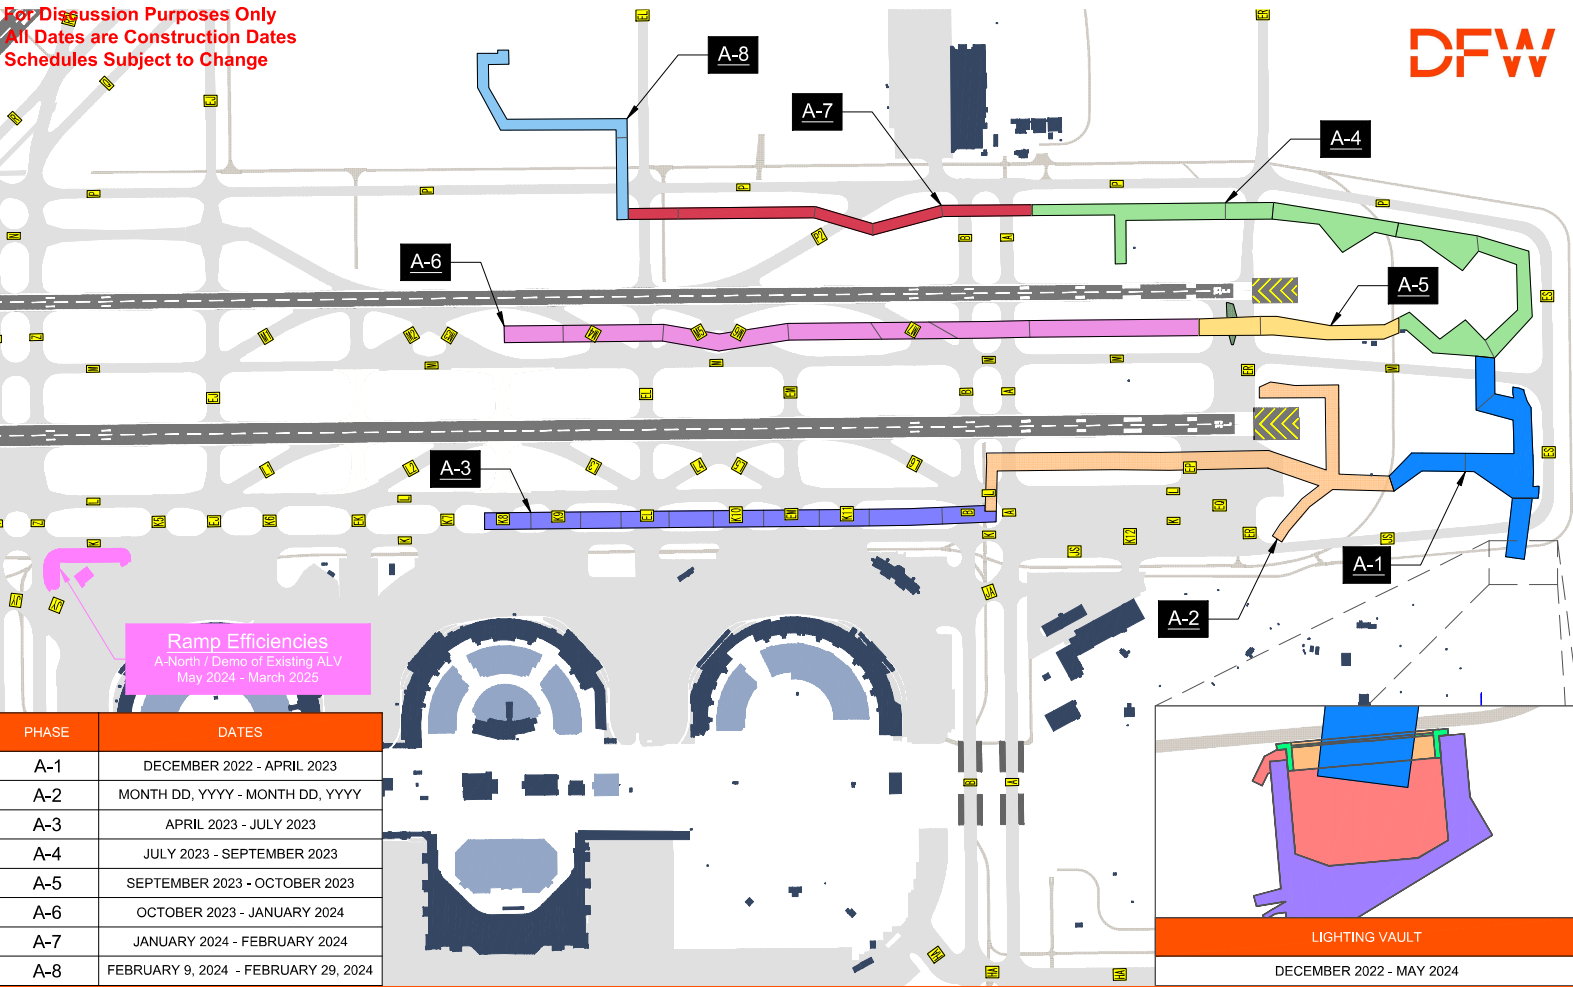

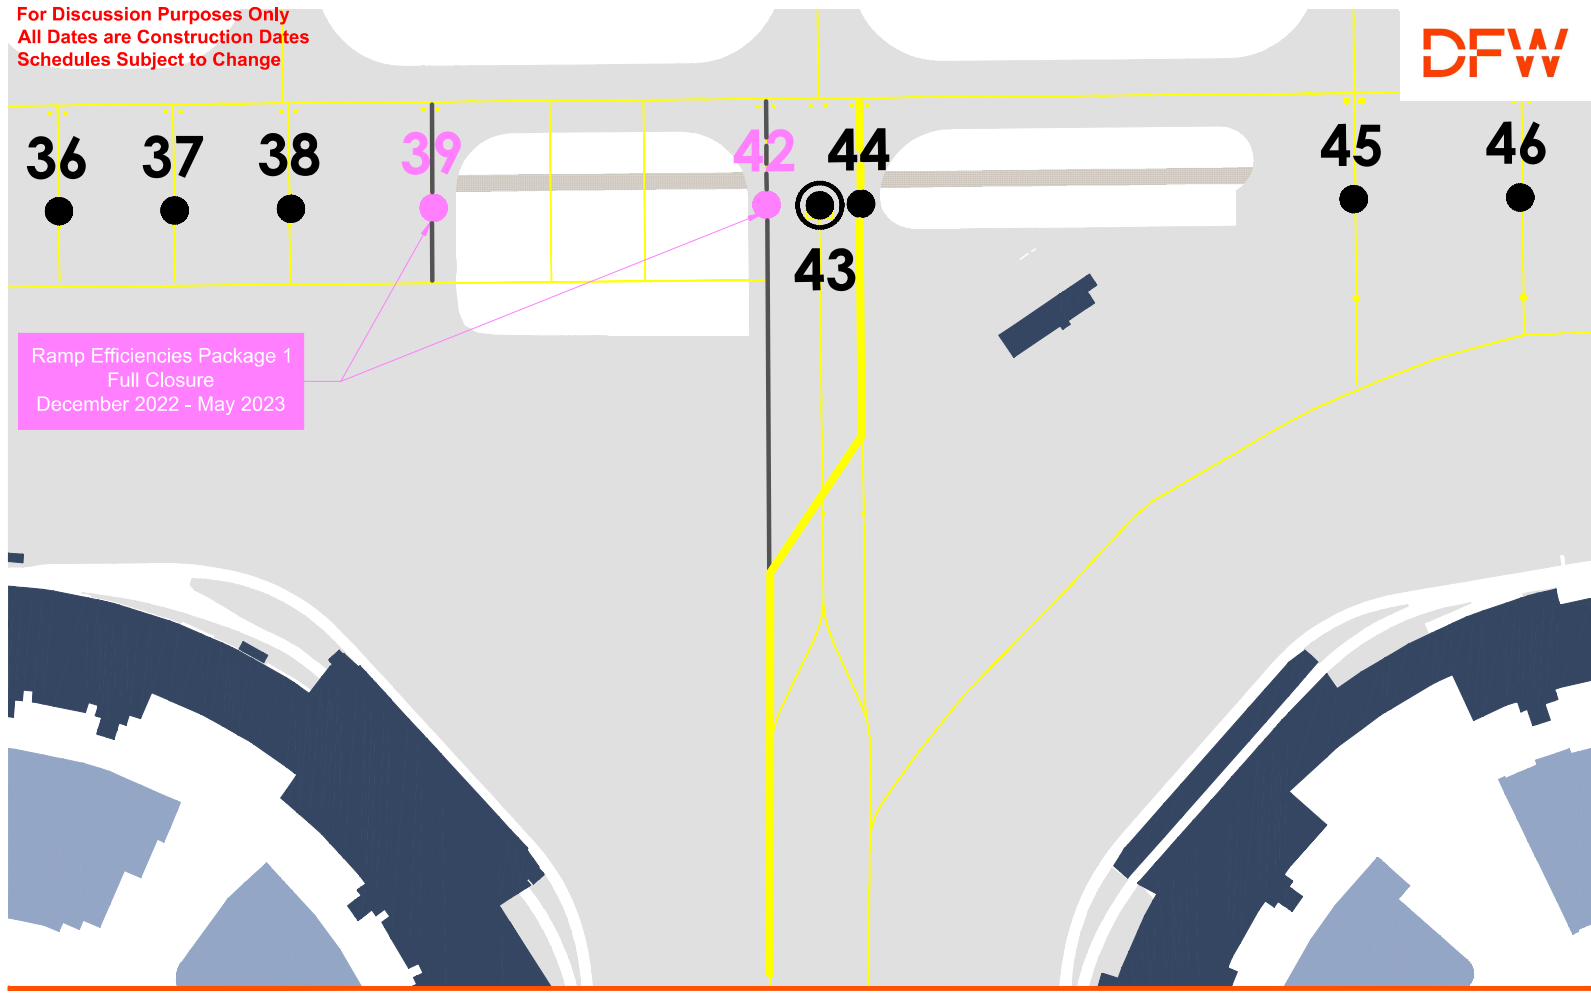


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

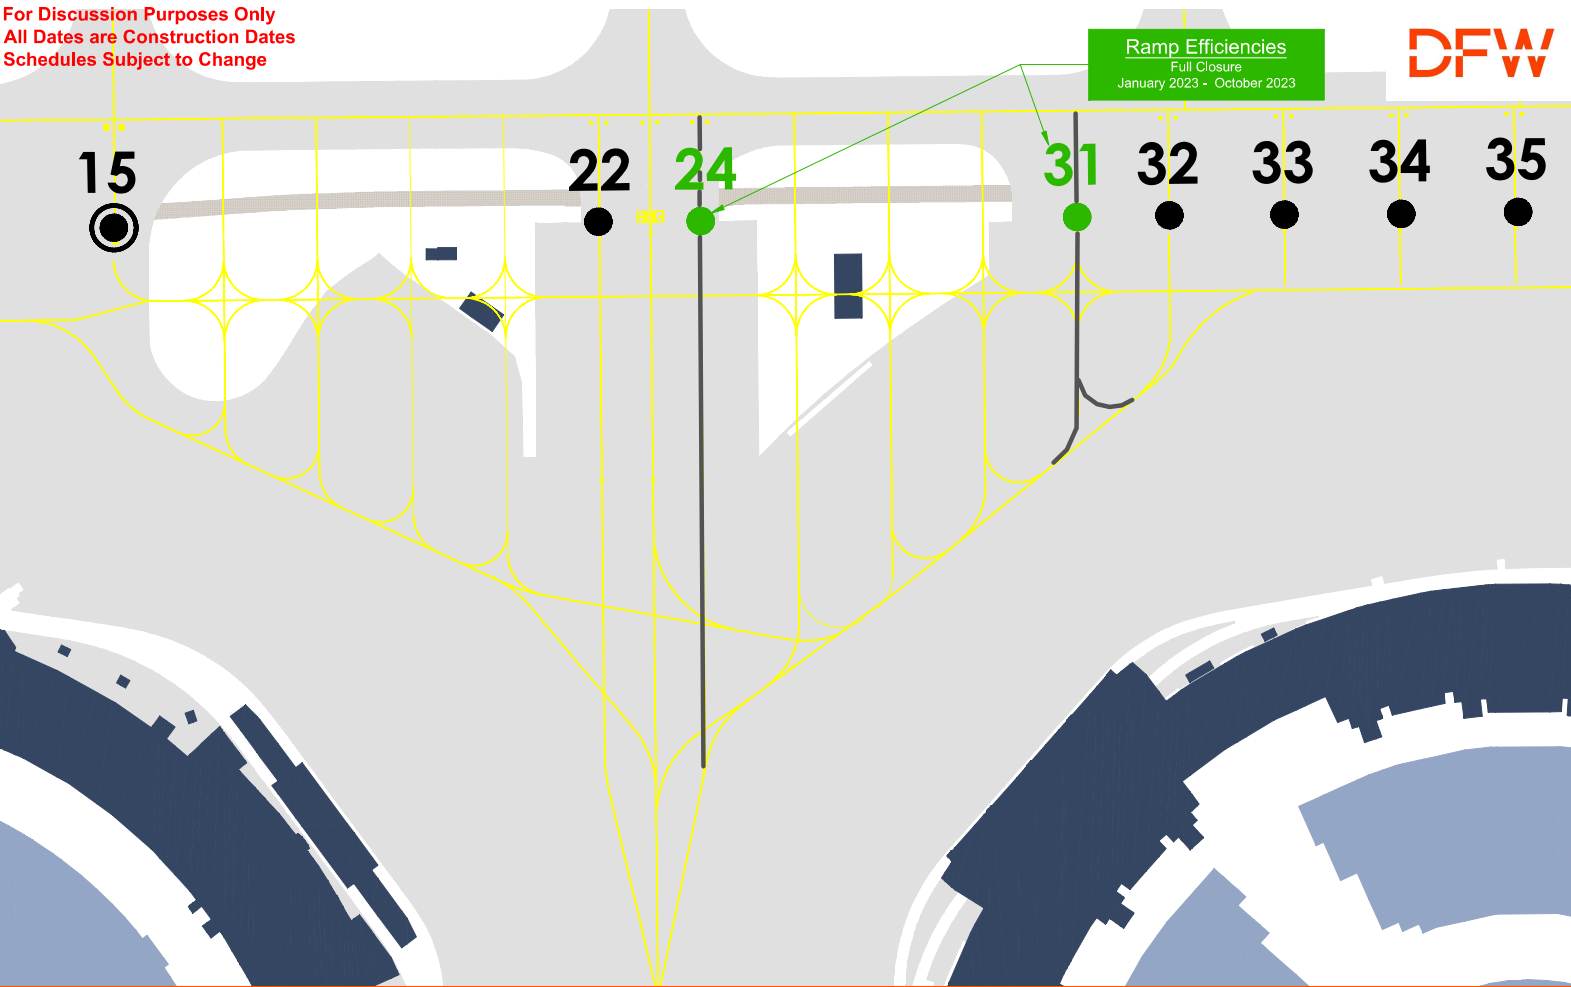


For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

DFW

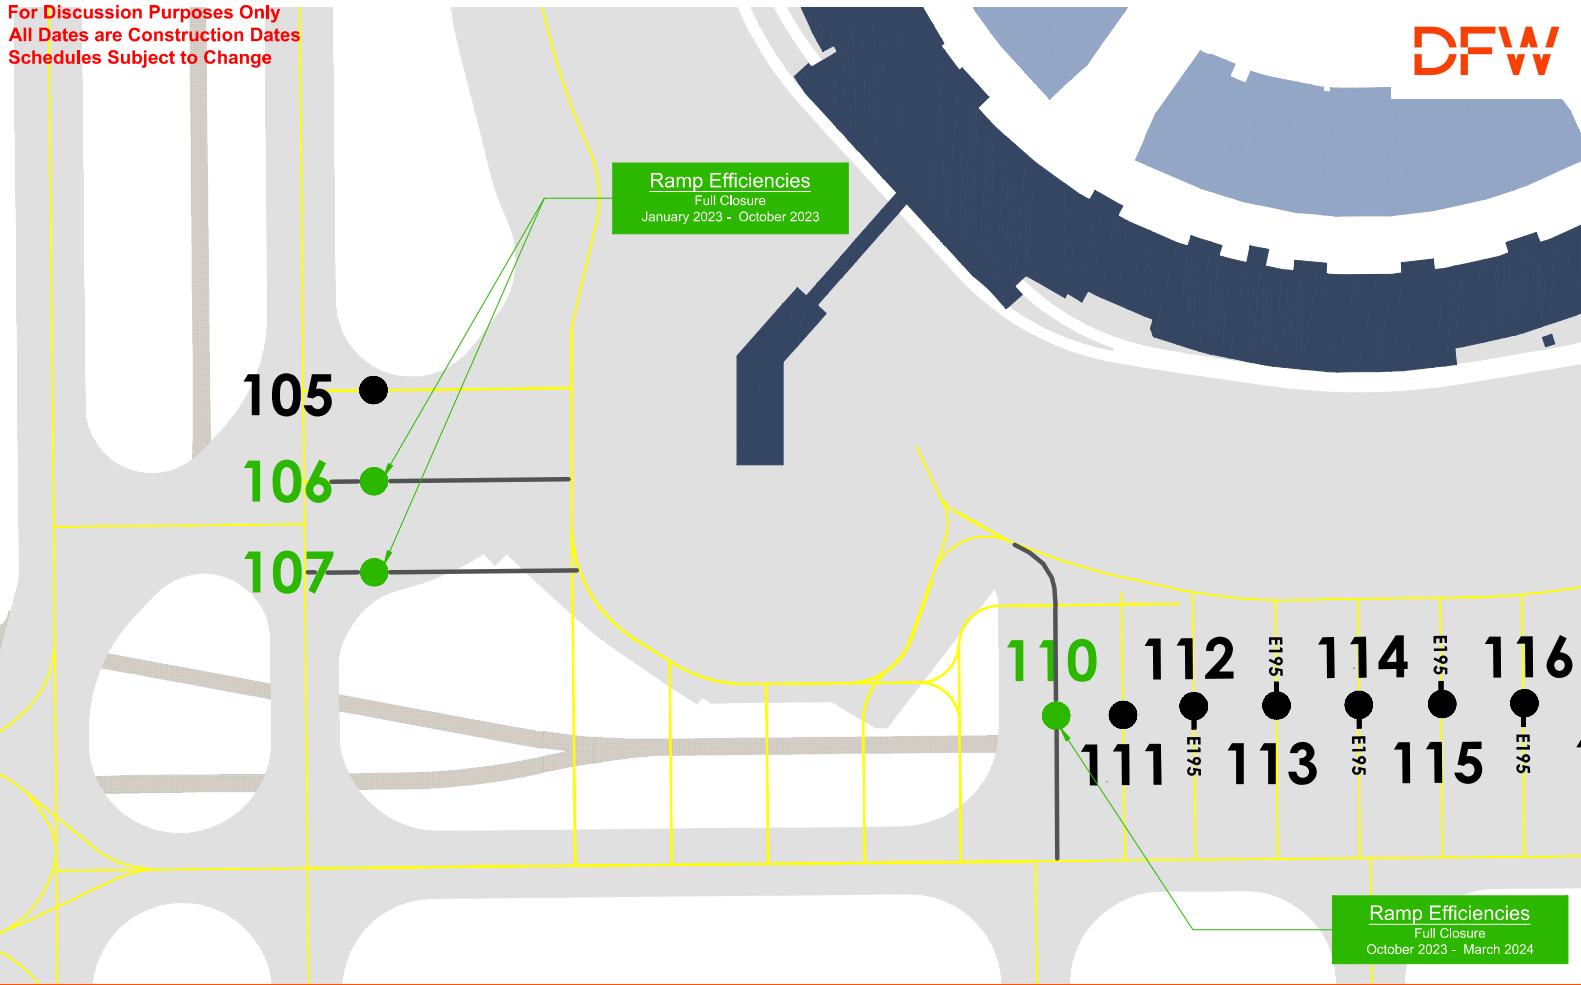

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

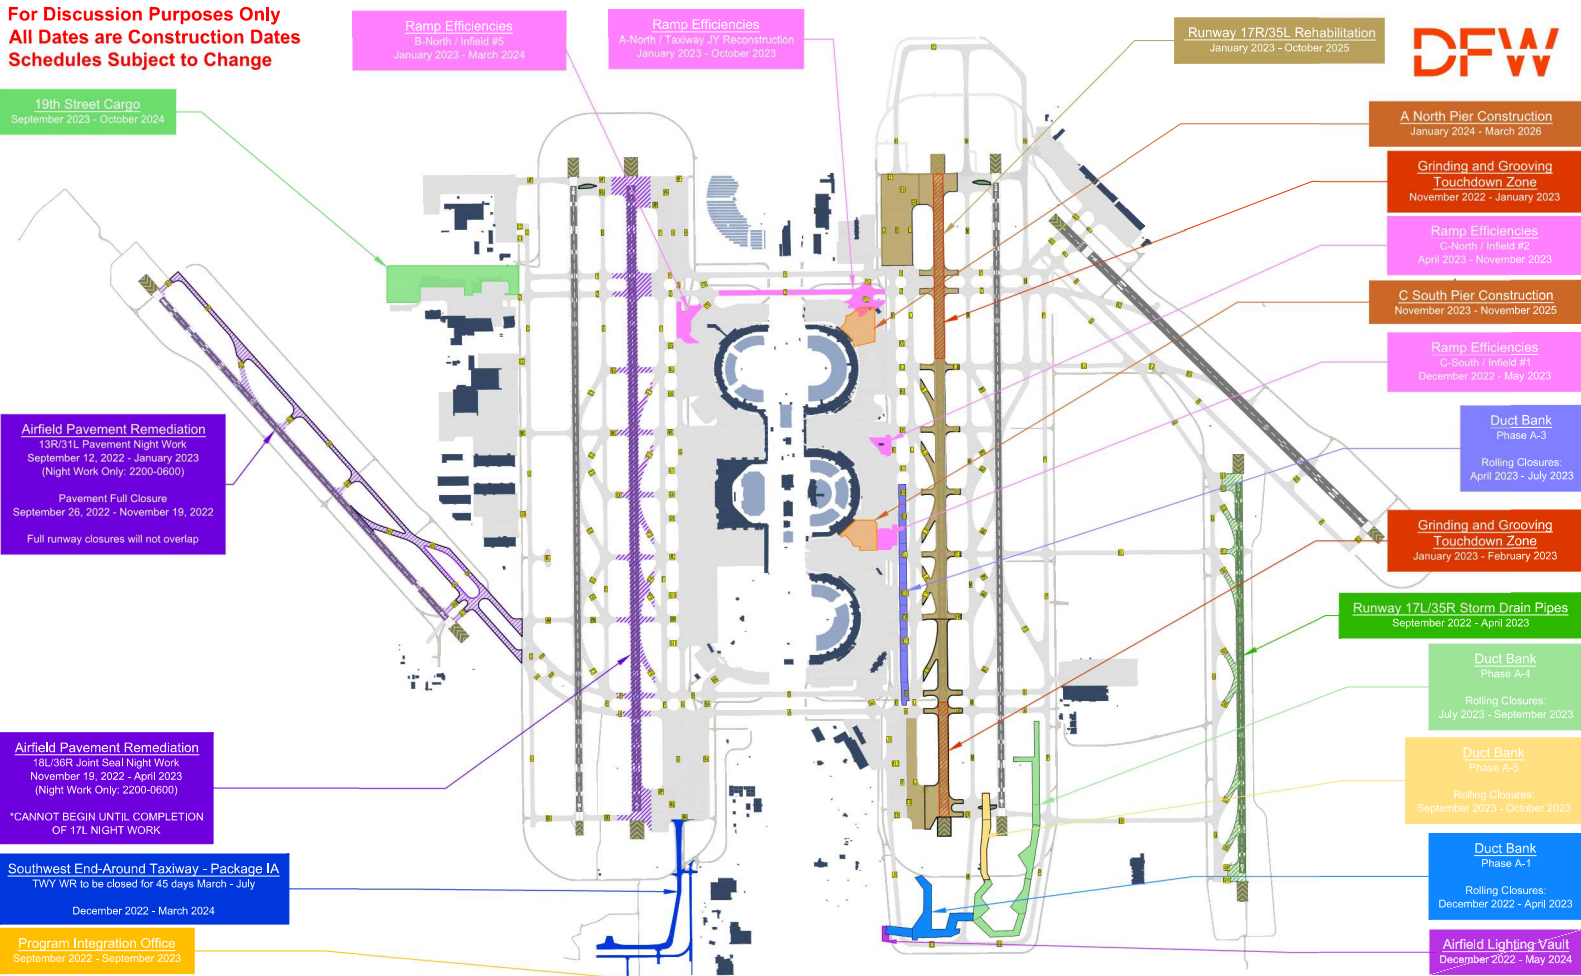

For Discussion Purposes Only
All Dates are Construction Dates
Schedules Subject to Change

